



TOWN HALL STATION COMMUNITY REFERENCE GROUP

CROSS YARRA PARTNERSHIP
FRIDAY 13 MARCH 2020





TOWN HALL STATION COMMUNITY REFERENCE GROUP

Jodie Barrington, CBD Precinct Lead, CYP D&C

Blythe Chidgey, Town Hall Station Stakeholder Engagement Manager, CYP D&C



Construction partner:




AGENDA



1. Project overview
2. Town Hall Station Update

PROJECT OVERVIEW



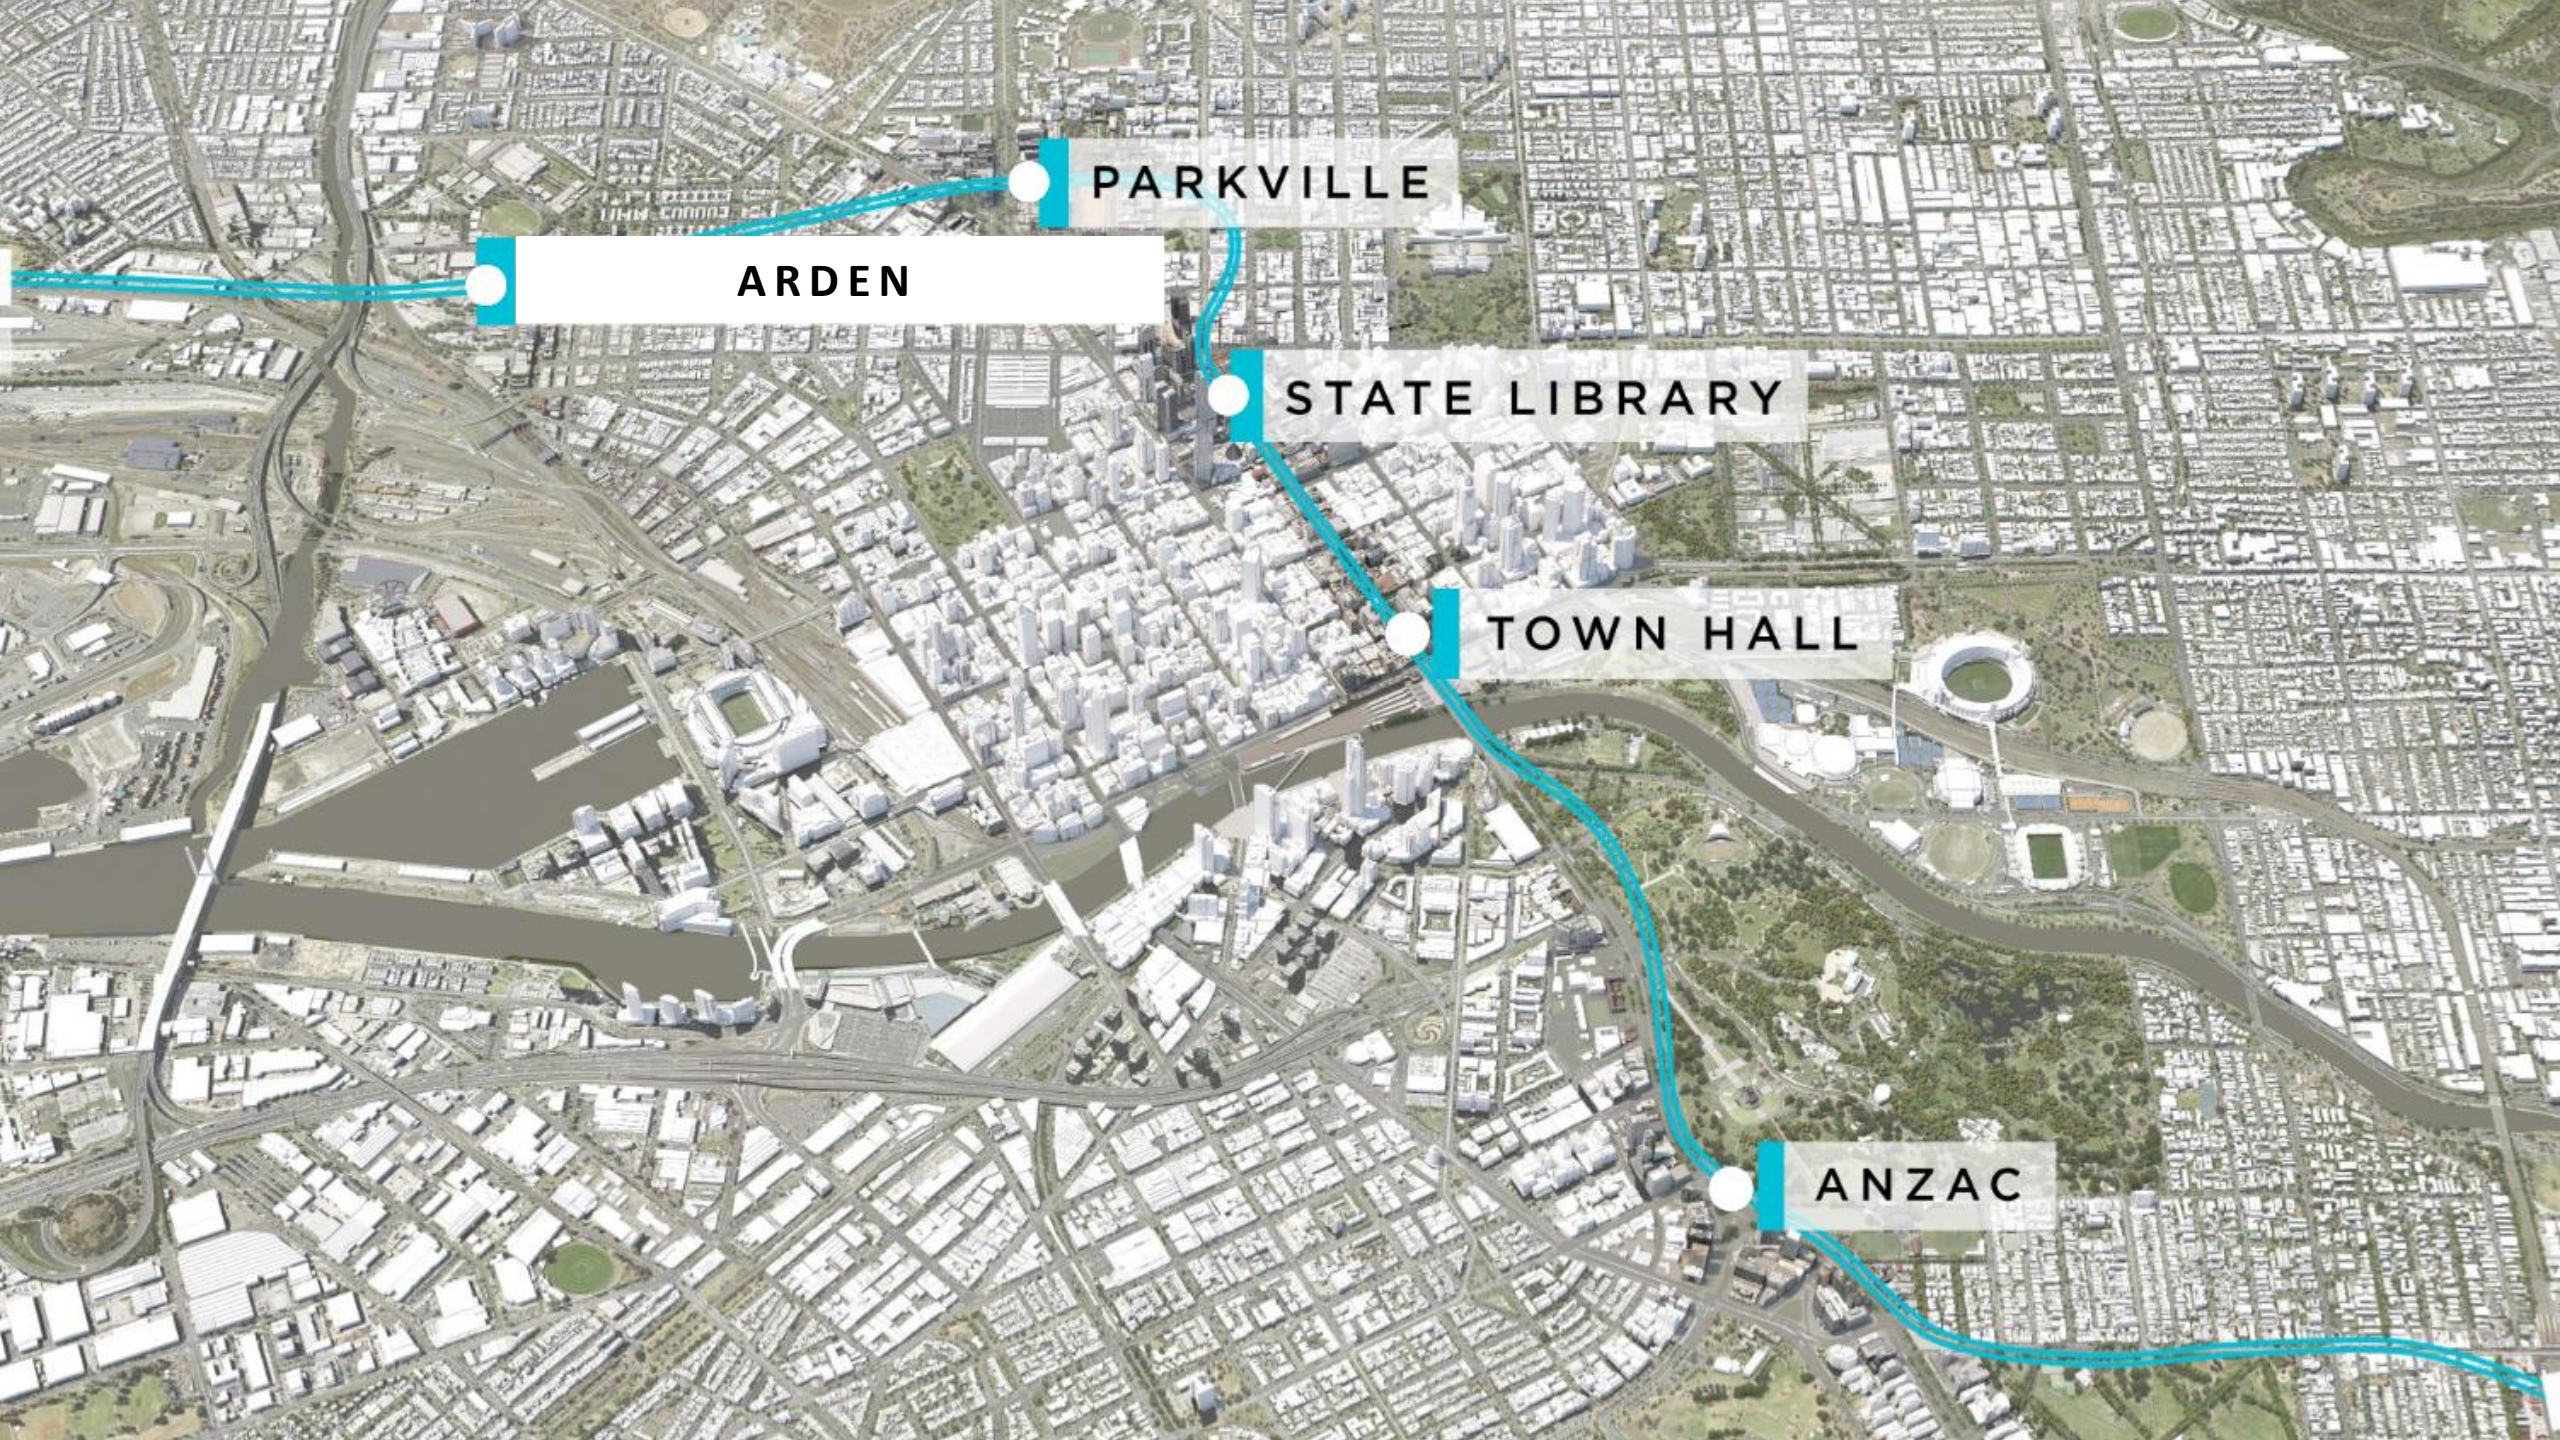

ARDEN

PARKVILLE

STATE LIBRARY

TOWN HALL

ANZAC


FIVE YEARS SINCE WORK BEGAN ON THE METRO TUNNEL PROJECT VIDEO



ROADHEADER TUNNELLING



CBD SOUTH ROADHEADERS

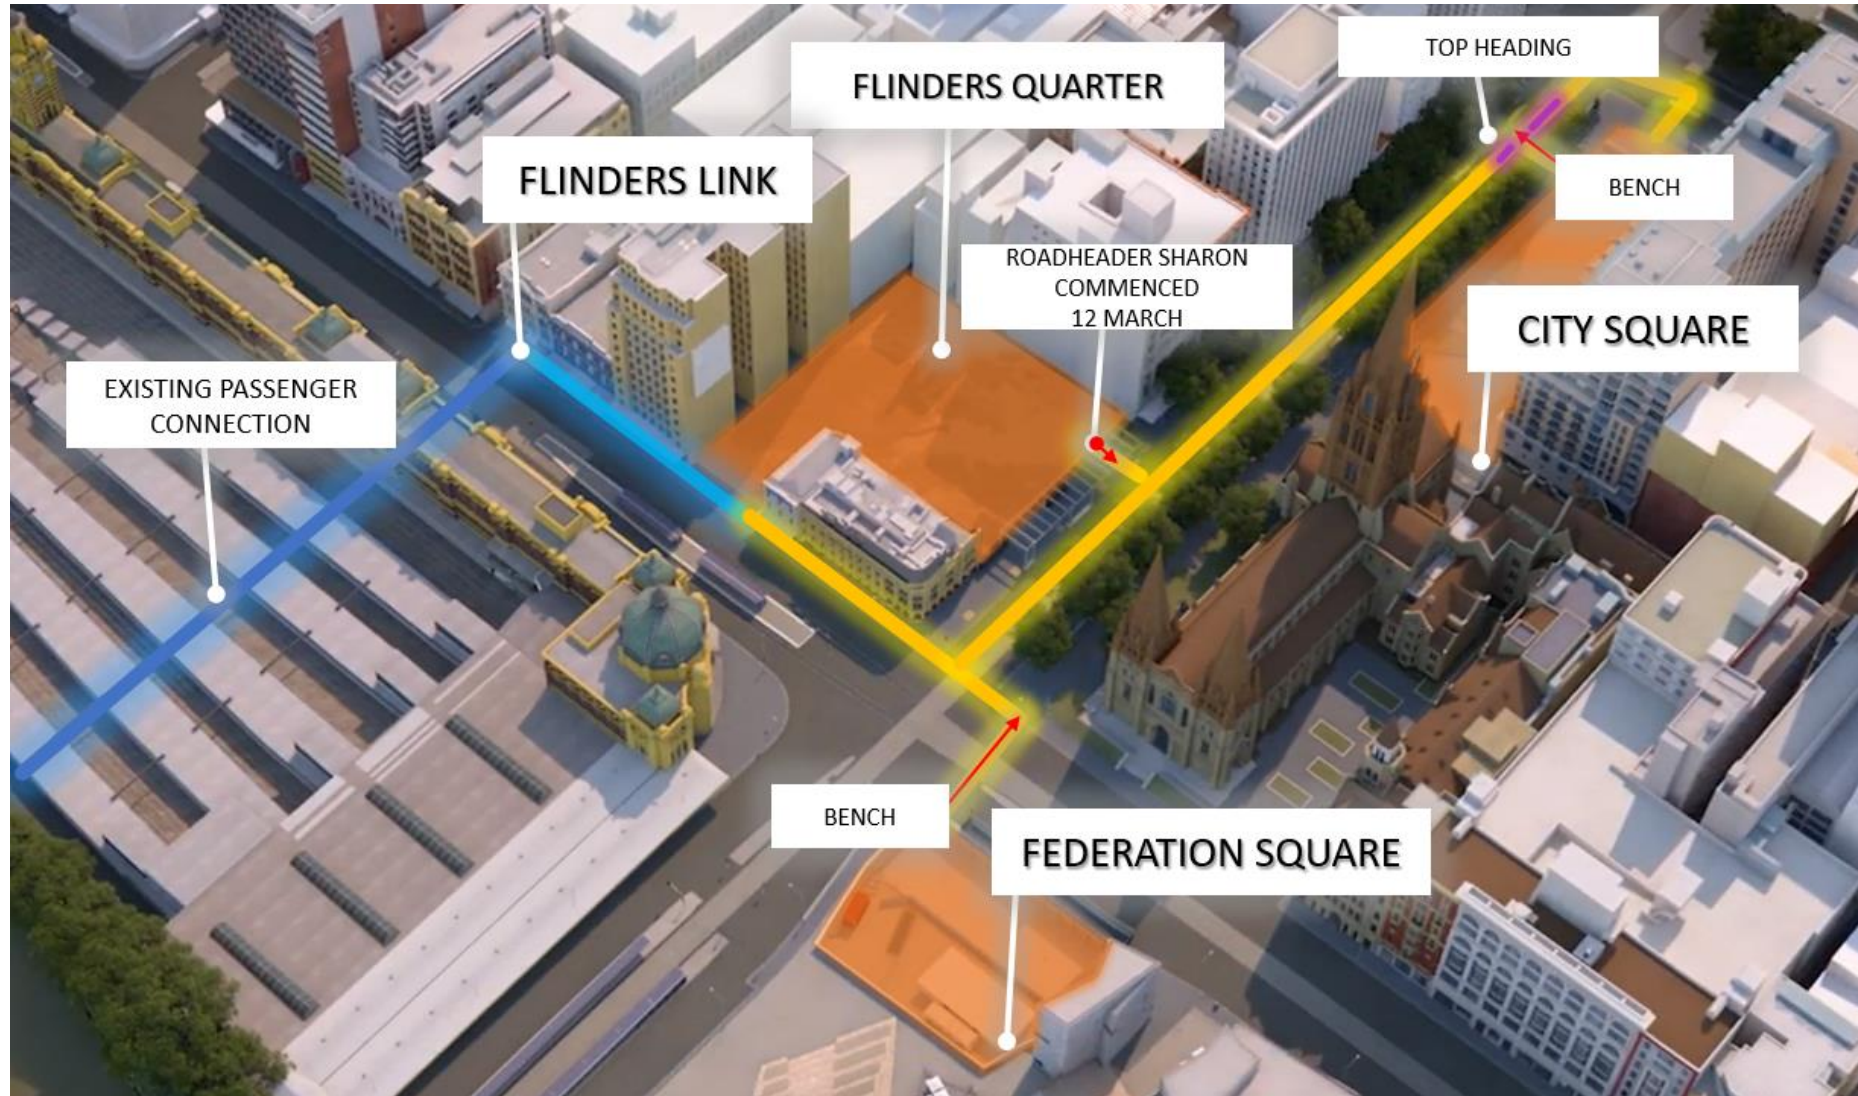

CITY SQUARE

- Completed 17 meters of the top heading (north) and 6 meters (south)

FEDERATION SQUARE

- Completed the first bench of the passenger adit
- A larger roadheader will be delivered to the site in March to commence the fire egress adit

FLINDERS QUARTER

- Roadheader 'Sharon' commenced this week

TOWN HALL STATION UPDATE



FLINDERS QUARTER




FLINDERS QUARTER – SHAFT A

Activity	Mar	Apr	May	Jun	Jul	Aug
Acoustic enclosure	—●					
Roadheader tunnelling	●—————					


Breakthrough to central cavern

FLINDERS QUARTER- SHAFT B

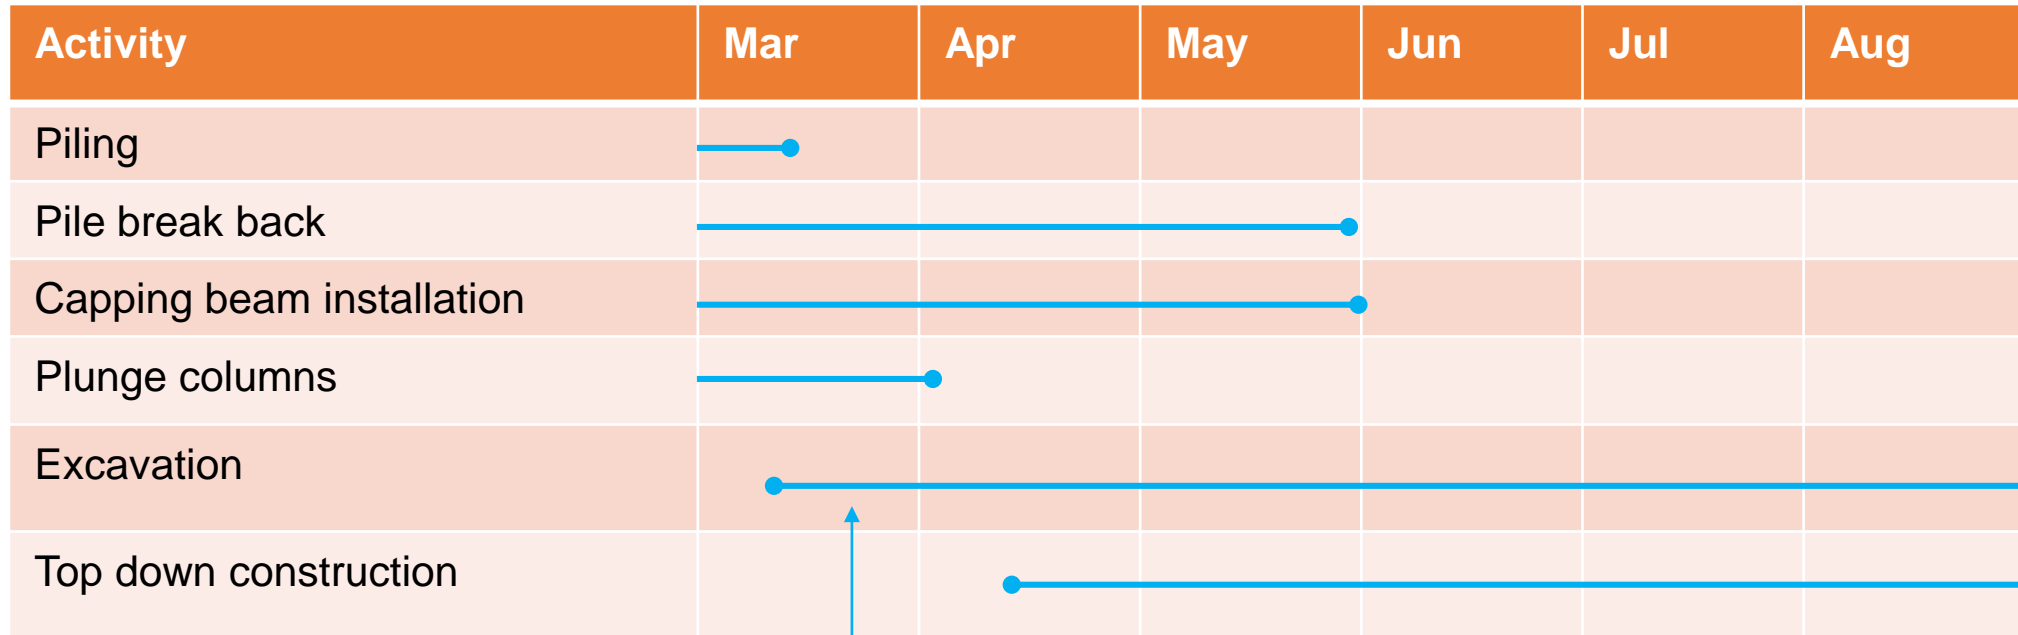

Slab break back

FLINDERS QUARTER

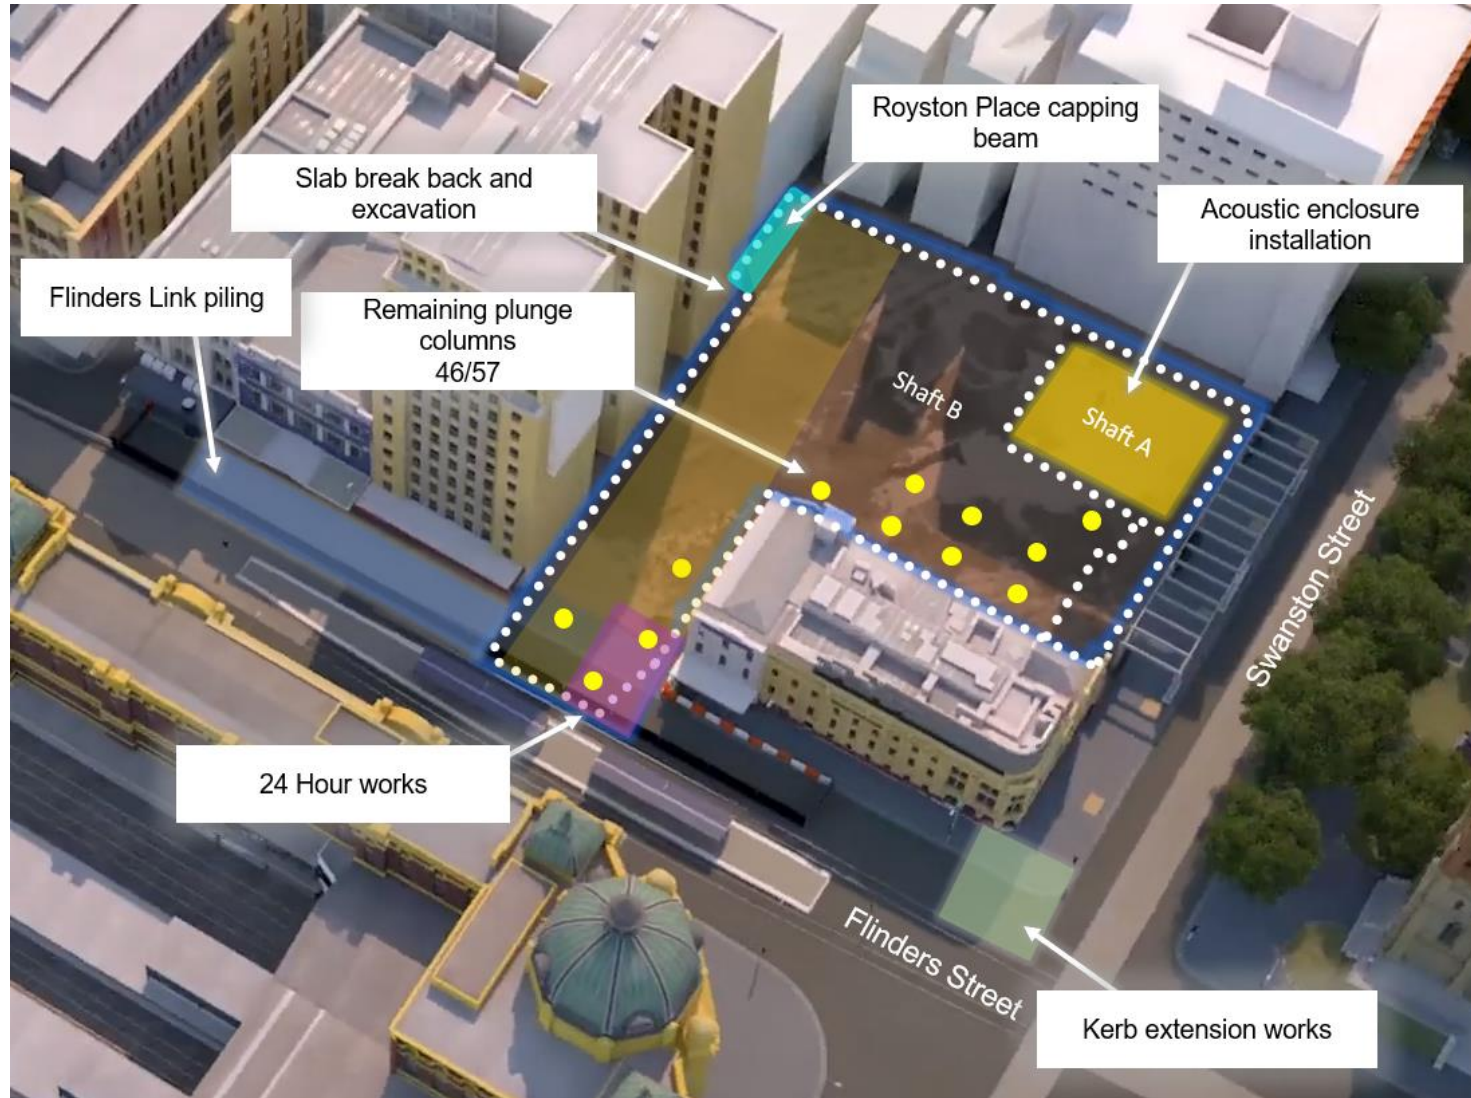

FLINDERS QUARTER – OUT OF HOURS WORKS

Deliveries (ongoing)

- Monday to Saturdays, 5am to 7am

Plunge columns

- Monday to Fridays, 7am to 10pm (*low noise clean up activities until 11pm as required*)
- Saturdays, 7am to 5pm

Roadheader tunneling

- Monday to Sunday, 7am to 10pm

Excavated material removal and piling

- Sundays, 8am to 4pm

Clamshell Excavation


- Monday to Fridays, 7am to 10pm
- Saturdays, 1pm to 10pm



FLINDERS LINK

TRAM OCCUPATION FLINDERS STREET


24 hours, from 1:30am Monday 23 March until 4:30am Monday 30 March 2020

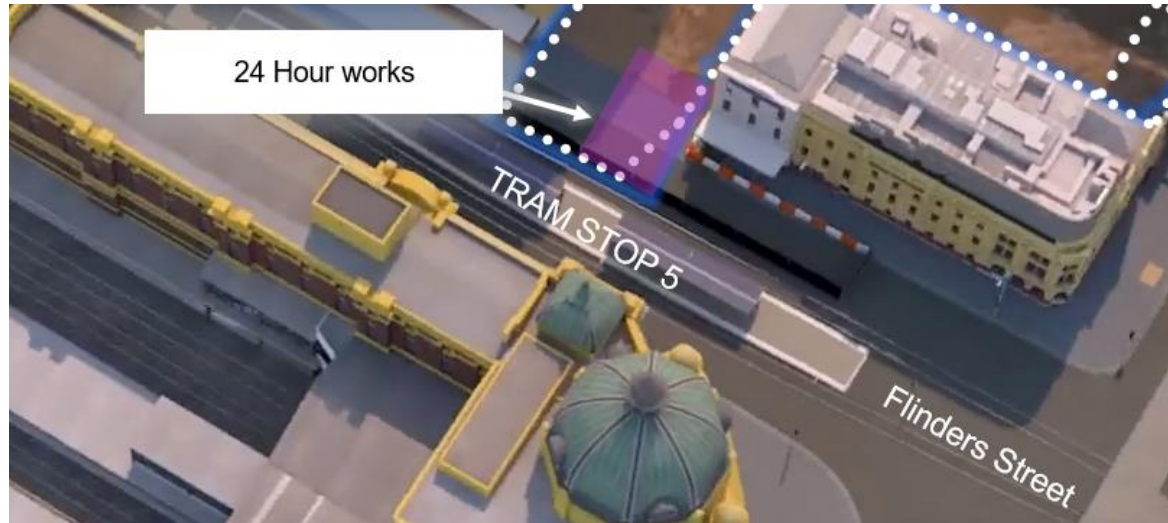

- Excavation
- Pile break back
- Cable installation
- Pour capping beam
- Hard hoarding installation


- Route 70, 75 and City Circle tram services will be disrupted from the first tram service on Monday 23 March until the last tram service on Sunday 29 March

FLINDERS LINK WORKS UPDATE

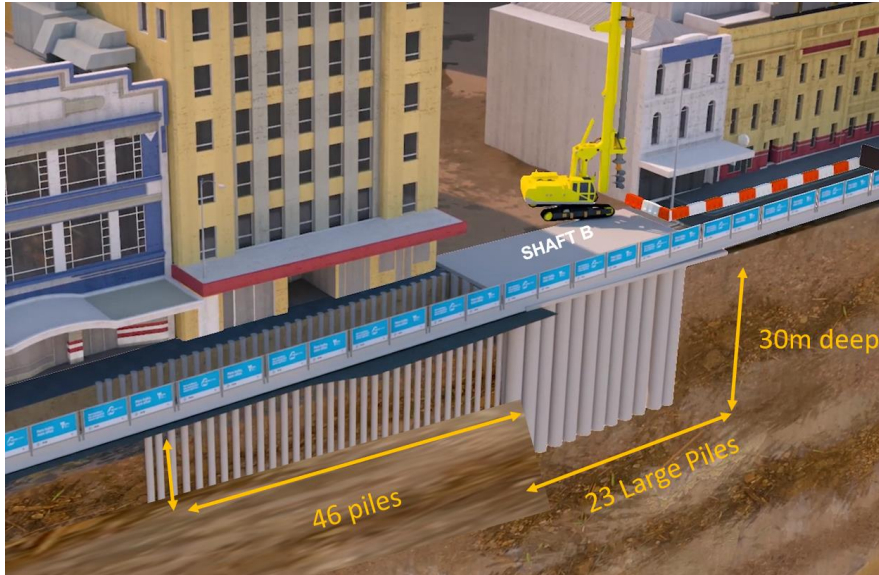

Activity	Mar	Apr	May	Jun	Jul	Aug
Service relocation works	—●					
Excavation			●—●	—●		
Piling		●—●				
Tram Occupation	●—●					

Slab break back

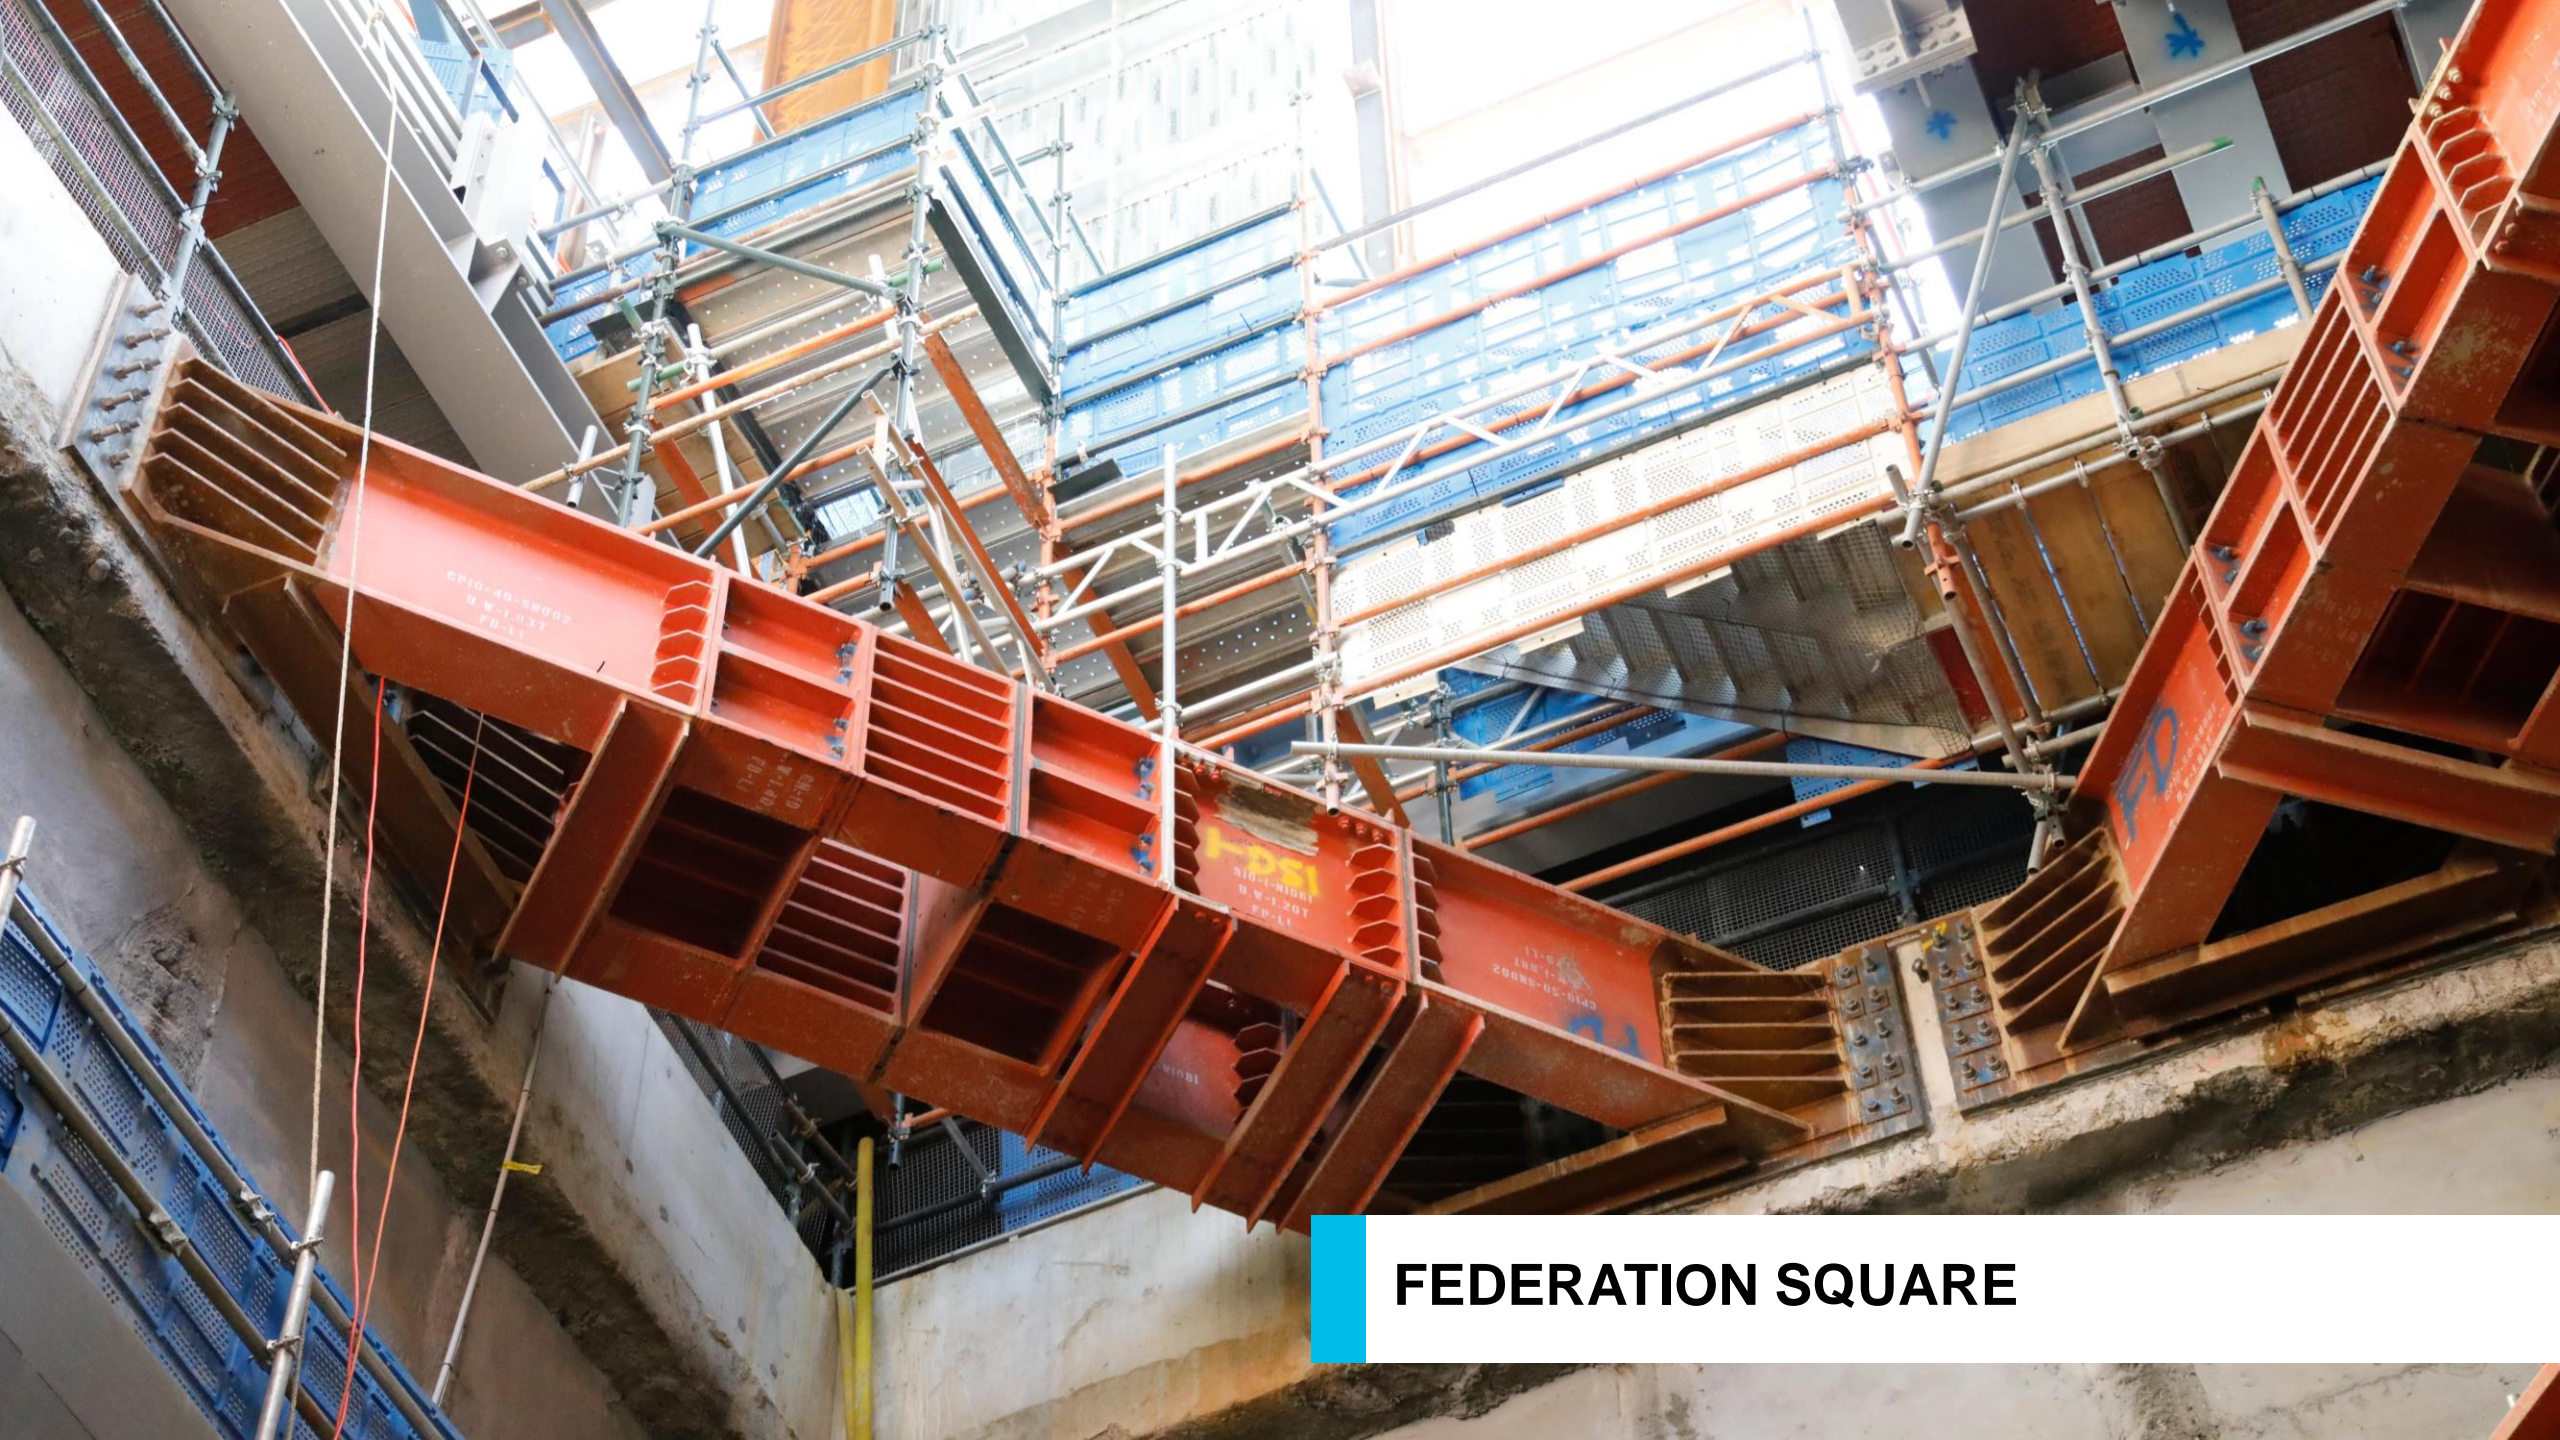

FEDERATION SQUARE

FEDERATION SQUARE WORKS UPDATE

Activity	Mar	Apr	May	Jun	Jul	Aug
Acoustic shed construction						
Excavation						
Roadheader tunnelling						

Complete by 22 March

FEDERATION SQUARE – OUT OF HOURS WORK

Tunnelling and excavation

- 24 hours, Monday to Sunday

Acoustic shed construction

- 24 hours, Saturday to Monday

Roadheader delivery

- 10pm to 5am, mid-March


Acoustic shed roller door installation

- 10pm to 5am, Sunday 22 March



CITY SQUARE

CITY SQUARE WORKS UPDATE

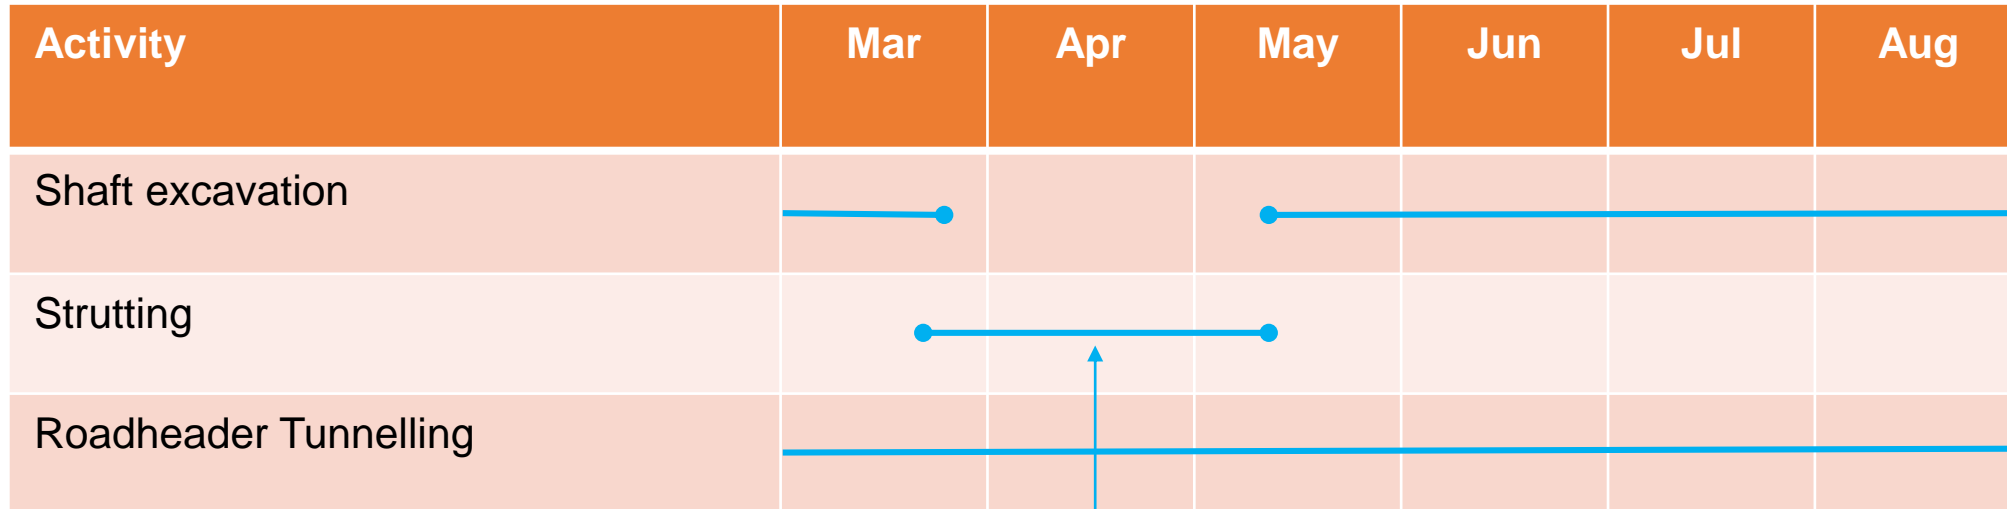

Next two levels of struts

CITY SQUARE – OUT OF HOURS WORKS

Tunnelling and excavation

- 24 hours, Monday to Sunday

Strutting

- 24 hours, Monday to Sunday

MONITOR INSTALLATION WORKS

MONITOR INSTALLATION WORKS




Indicative only

TRAFFIC UPDATE



KERB EXTENSION WORKS

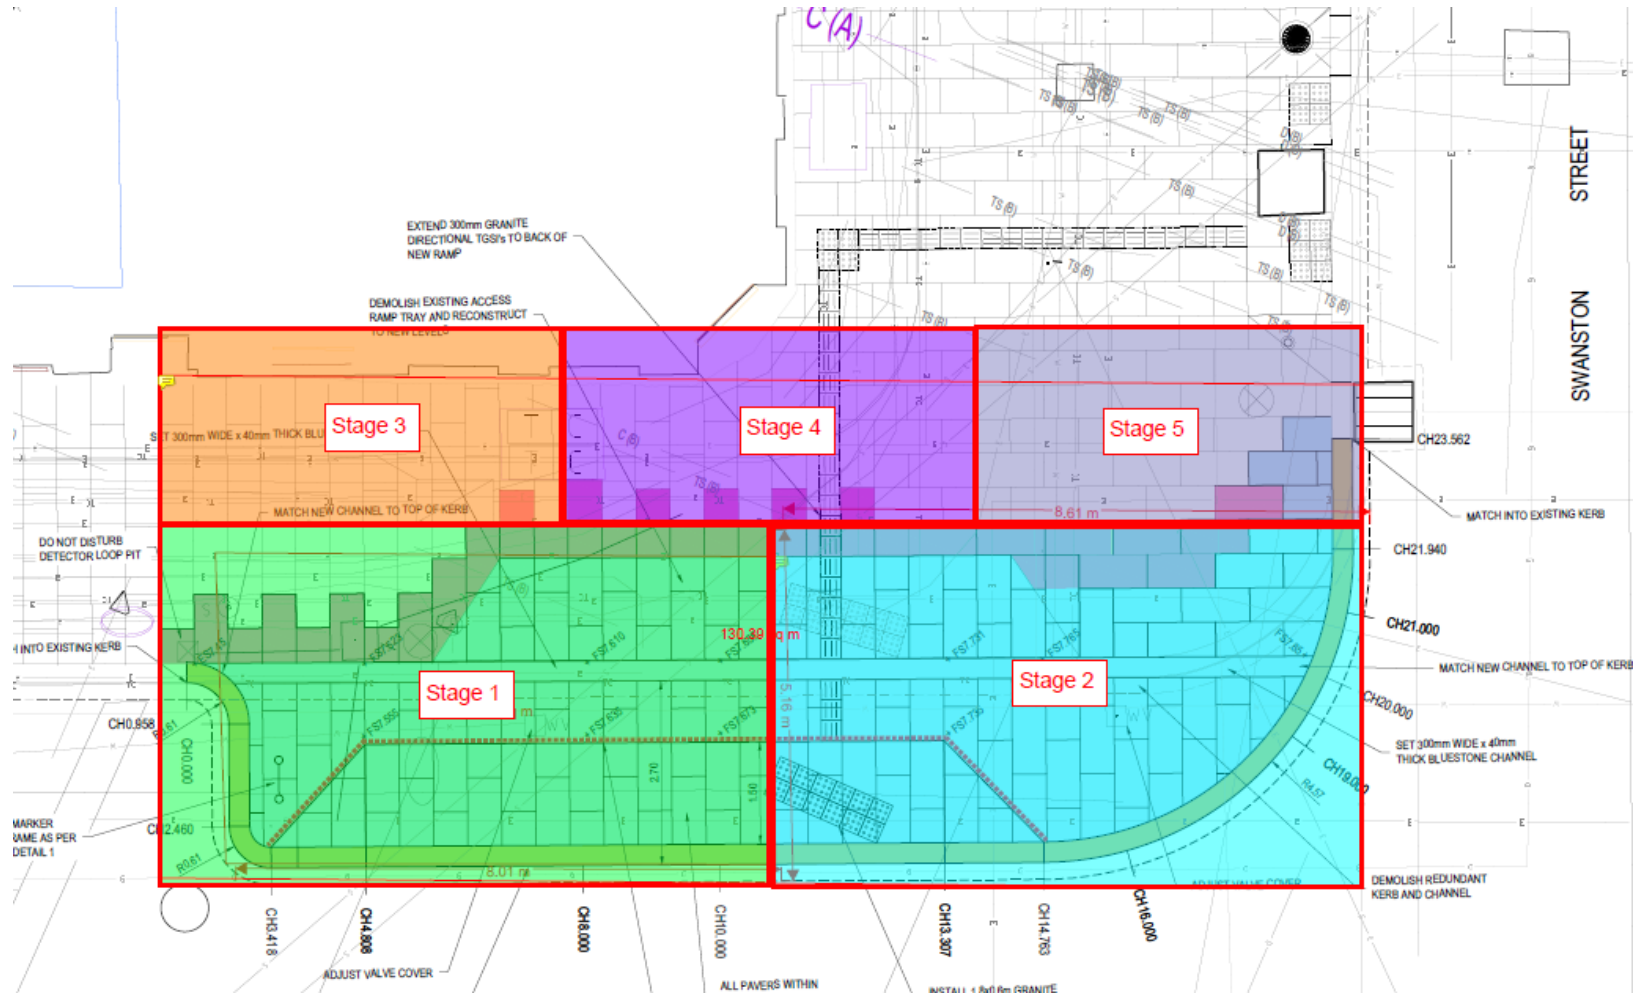

QUESTIONS?

