

#### **DOMAIN PRECINCT**

Community Reference Group

**Presentation by CYP** 

5 June 2024









#### **ACTIONS AND ISSUES REGISTER**



| #     | ACTION / ISSUE   | OWNER |
|-------|--|-------|
| A54-1 | CYP to provide an update on road safety concerns expressed by the CRG.                     | CYP   |
| A54-2 | CYP to provide an update on planting in the next meeting.                                  | CYP   |
| A54-3 | CYP to provide an update on the handover of public spaces and their opening to the public. | СҮР   |



# WORKS UPDATE: STATION CONSTRUCTION

### **WORKS UPDATE**ST KILDA ROAD REINSTATEMENT





- Final northbound
  asphalting was completed
  on Friday 31 May
- On street parking adjacent to The Botanica will be reinstated following the completion of footpath works
- Works to complete the left turn from St Kilda Road southbound into Domain Road expected in June

## WORKS UPDATE STATION WORKS










- Works on concourse level are nearing completion
- Testing of systems, including fire matrix testing is now underway
- Paving works are underway on the stairs

## **WORKS UPDATE**SHRINE OF REMEMBRANCE ENTRANCE



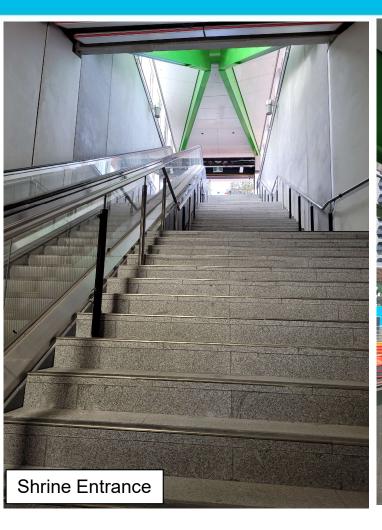



- Electrical and plumbing connections into the station are complete
- Retaining wall construction around the forecourt perimeter
- The service elevator to the concourse level and along with covered walkways have now been removed
- Works have begun on the landscaping between Cobbers Memorial and St Kilda Road

## **WORKS UPDATE**ALBERT ROAD RESERVE STATION ENTRANCE









- Formwork and concrete pour is now complete on the stairs leading from the station entrance down to Albert Reserve
- Paving is progressing from north to south at the station forecourt
- South African Soldiers Memorial scaffolding is at its final height and the reconstruction is expected to be complete next month
- Works will commence this month on the construction of the Albert Road
   South connection into St Kilda Road.

## **WORKS UPDATE**CENTRE MEDIAN, CHILLER PLANTS AND STATION VENTILATION






- Low level planting is now complete in all sections of the St Kilda Road centre median
- Tree planting through the centre median will now commence (City of Melbourne)
- Chiller plant is now fully functional, operational noise testing is expected in late July 2024

### **WORKS UPDATE**DOMAIN ROAD AND EDMUND HERRING OVAL



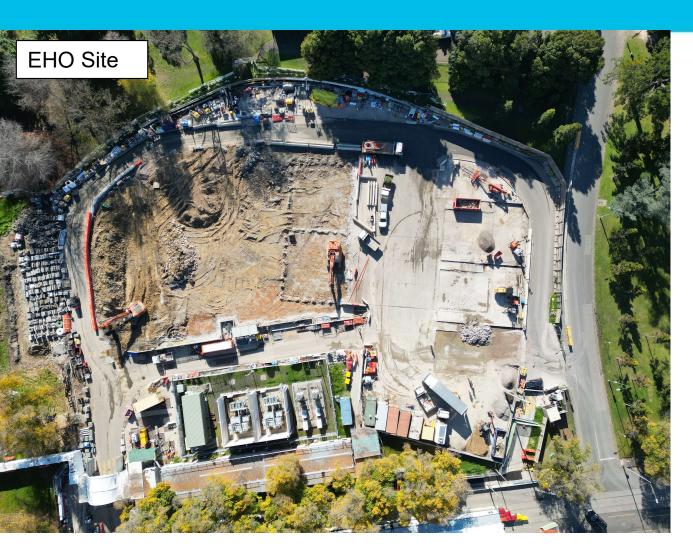

- Construction of the new dual-purpose bus/tram stop has now commenced
- Demolition of the concrete hard stand on Edmund Herring Oval (EHO) is progressing
- The electrical substation is decommissioned and will be removed from site in the coming weeks



#### **ENVIRONMENT UPDATE**

#### **NOISE MONITORING**

**Edmund Herring Oval Site Demolition** 





#### **Domain Rd** → **EHO Demolition** 15min LAeq (7am - 6pm) **Receiver** Modelled **Monitoring** Hallmark 50-55dB 58-62dB **Domain Hill** 58-63dB 50-55dB **Domain** 60-65dB 55-60dB Botanica 65-70dB 55-60dB MGS 65-70dB 67-74dB



#### PROJECT WIDE UPDATE

