



TOWN HALL STATION COMMUNITY REFERENCE GROUP

CROSS YARRA PARTNERSHIP D&C

Kate Walshe, Communications and Stakeholder Engagement Director, CYP D&C

Mary Parker, Director Communications & Creative, CYP Project Co

Blythe Chidgey, Town Hall Station Stakeholder Engagement Manager, CYP D&C

Andrew Cox, Flinders Quarter Project Manager, CYP D&C

19 November 2021



Agenda




1. Project Overview
2. Creative Program Update
3. Town Hall Station Update
4. Flinders Link: Flinders Street Staging Update

Project Overview

Precinct Updates

Metro Tunnel Project

Project Alignment

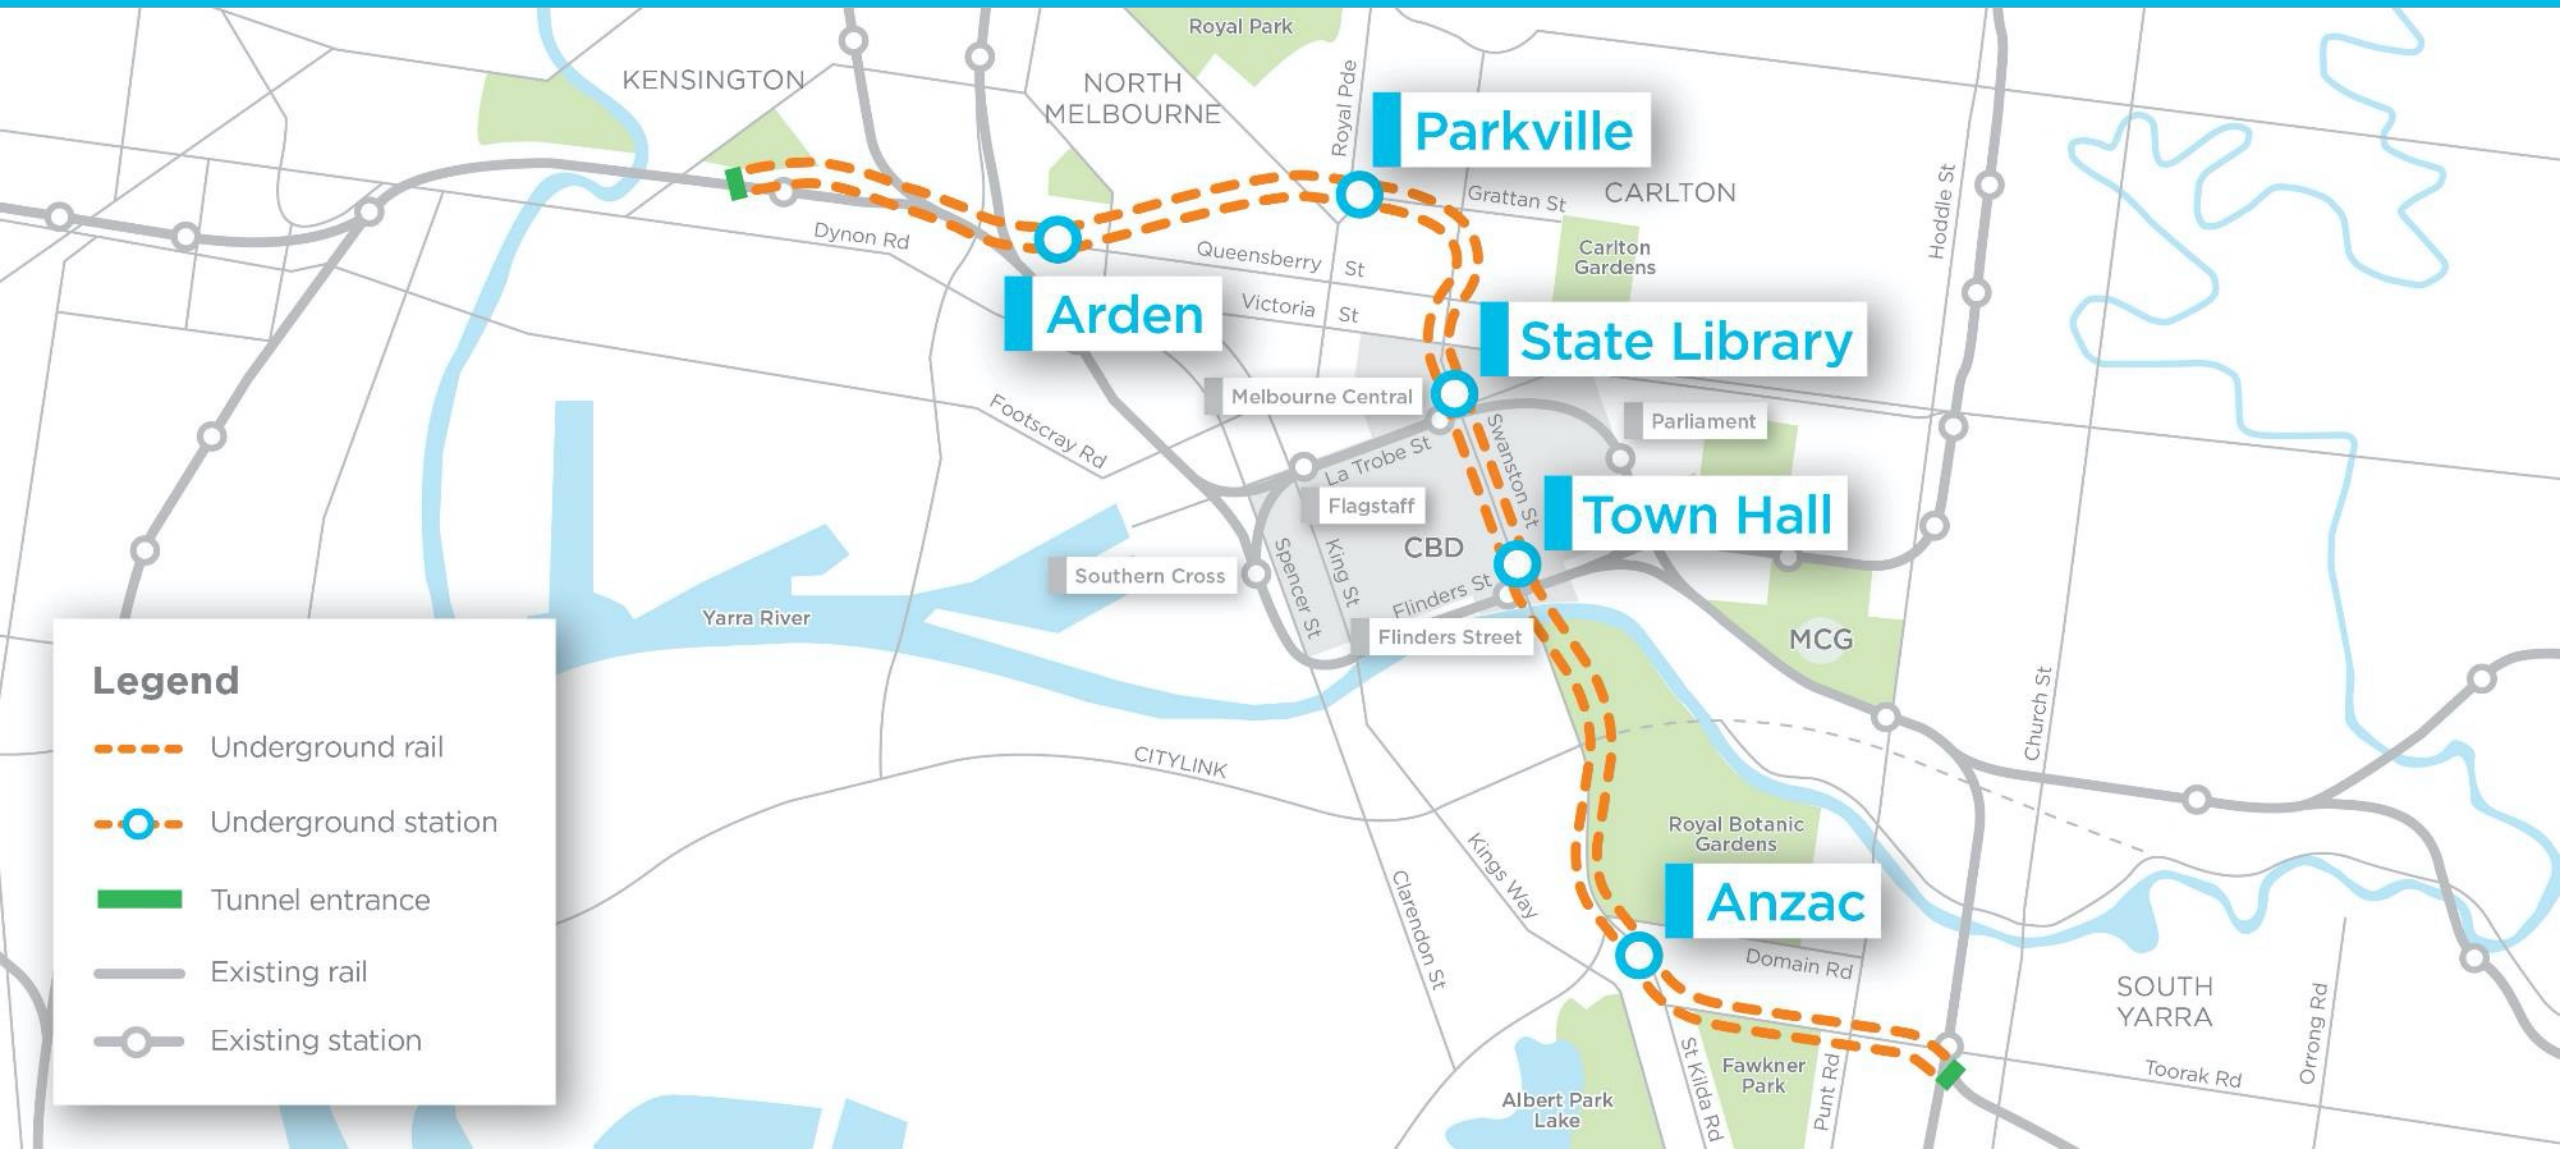

Arden Station



- All 45 segments of the Arden Station entrance arches have now been installed
- Approximately 80% of the platform has been constructed, with works ongoing
- Blockwork installation and mechanical, electrical and plumbing installation is continuing.



Parkville Station



- Excavation of Grattan Street West
- Construction of Royal Parade pedestrian underpass underway with the recent arrival of roadheader Melinda to site
- Blockwork wall construction and services installation are taking place in the main station box



State Library Station



- Shaft construction is progressing at the La Trobe Street site as B3 excavation continues. Above ground, steel fixing is now underway for the buildout of the station entrance
- At Little La Trobe Street site, the B3 slab was poured in October and excavation of the B4 slab is now underway
- Internal wall reinforcement and strut removal are underway on Franklin Street.



Anzac Station



- The entire station box has now been completely excavated
- D-wall demolition is ongoing on both sides of the station box, connecting the concourse level of the station to two of the three station entrances
- In the tram interchange station entrance, the roof slab is now complete.



Creative Program

Update



Haus of Dizzy and Gammin Threads



Melbourne Fashion Week Pop-Up Runway



Federation Square Shed



Metro Tunnel Christmas – Scott Alley




Metro Tunnel Christmas – City Square



Metro Tunnel Christmas Performance

16 December

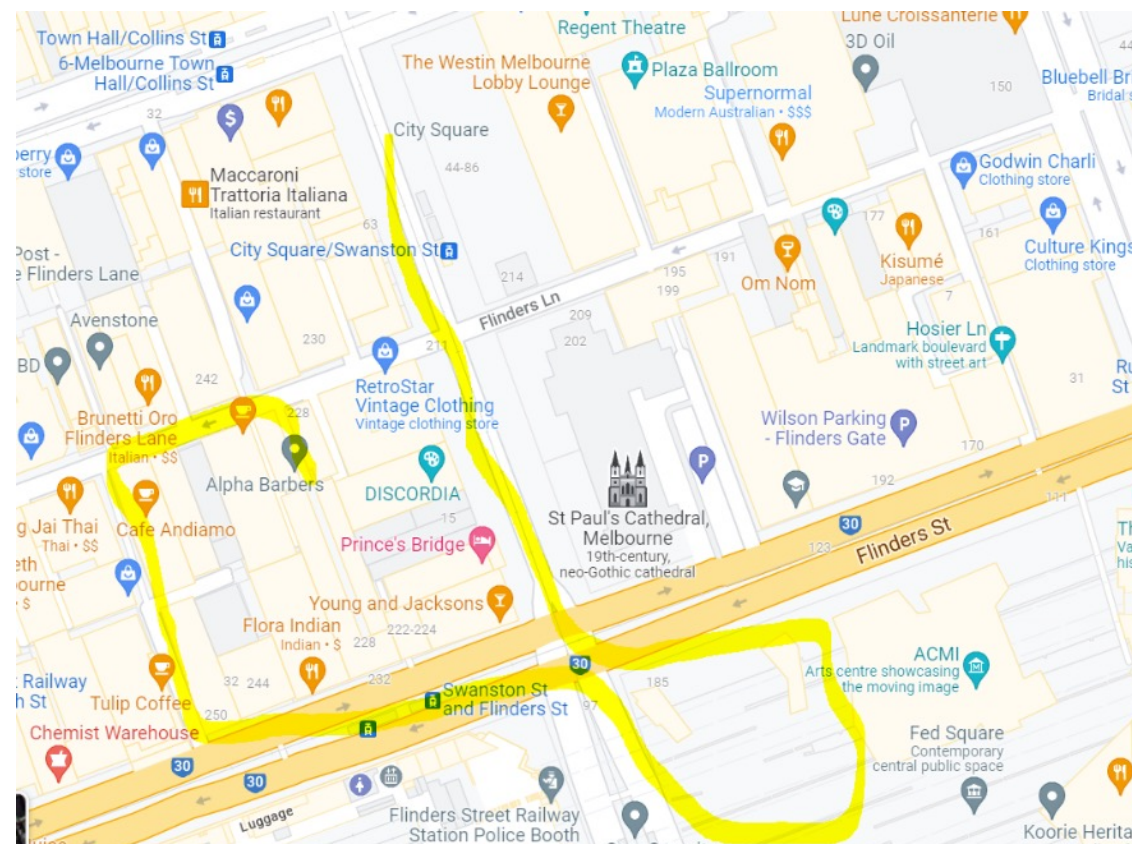


1. **Late November:** Huxleys and Electric Confetti artwork installed on City Square and Scott Alley
2. **Late November:** Huxleys Christmas Video at Federation Square
3. **December 4 and 5:** 'We built this City' at University Square
4. **December 16:** Huxleys performance
5. **January:** City Square artwork collaboration with ACCA for 'Who's afraid of public space?'
6. **January 23:** Miss First Nations / Midsumma artworks in Scott Alley.

Degraves Street

Signage Request

Welcome to Degrares New Signage

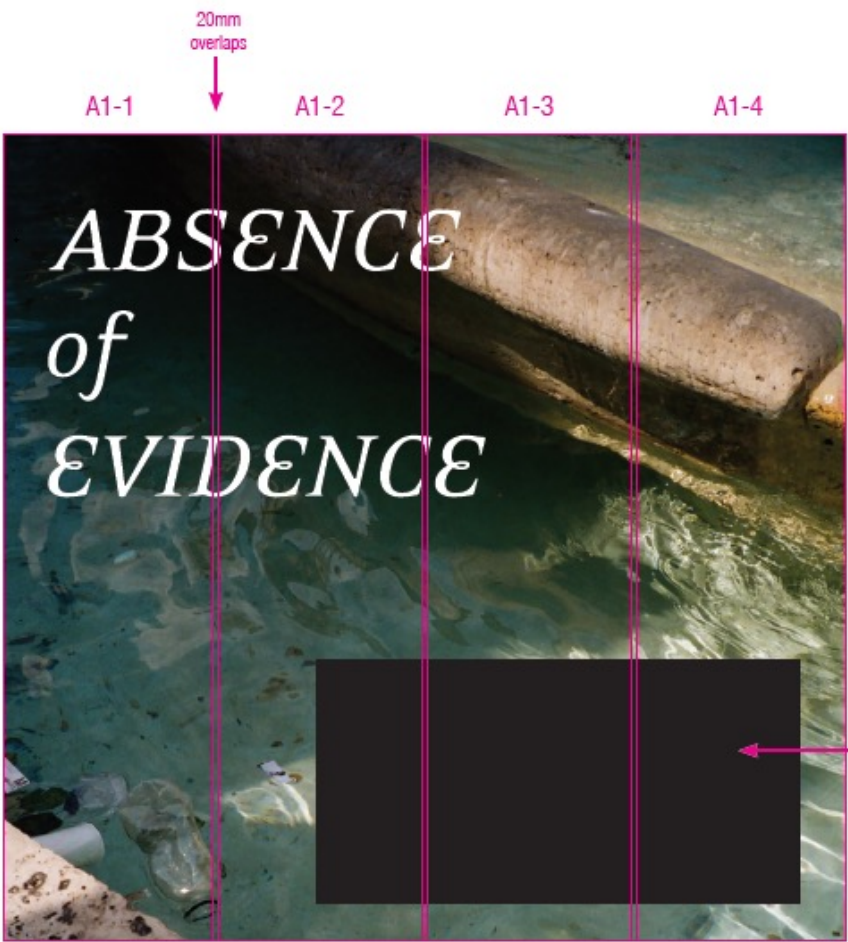

Area size = 4285mm(w) x 4100mm(h)
Final trim size = 4285mm(w) x 4100mm(h)

Screenshot
@100% scale



Installation Notes



Installer to trim around
Fire Hydrants on-site

Heritage and Sustainability

Initiatives

- Artist Pool EOI to receive one of five historic pieces of bluestone obtained via the archaeological dig
- Pieces allocated to: David Waters, Anton Hasell, Brett Ashby and James Carey/ Bridie Lunney
- Artists were invited to attend a session by Ochre Imprints to learn more about the site
- They all agree to the Creative Program sending a photographer to document outcomes.



- Curated by Craft Vic – an exhibition of works created by 8 artists using discarded material from the archaeological dig
- Approximate timing: October 2022
- Images (possibly studio/ WIP images of the work being made) will also be up in the Franklin Street frames.



Recycled Art Bags



Recycled art bags



Questions



Town Hall

Station Update

Town Hall Station

Central Platform and Rail Tunnels




City Square Site





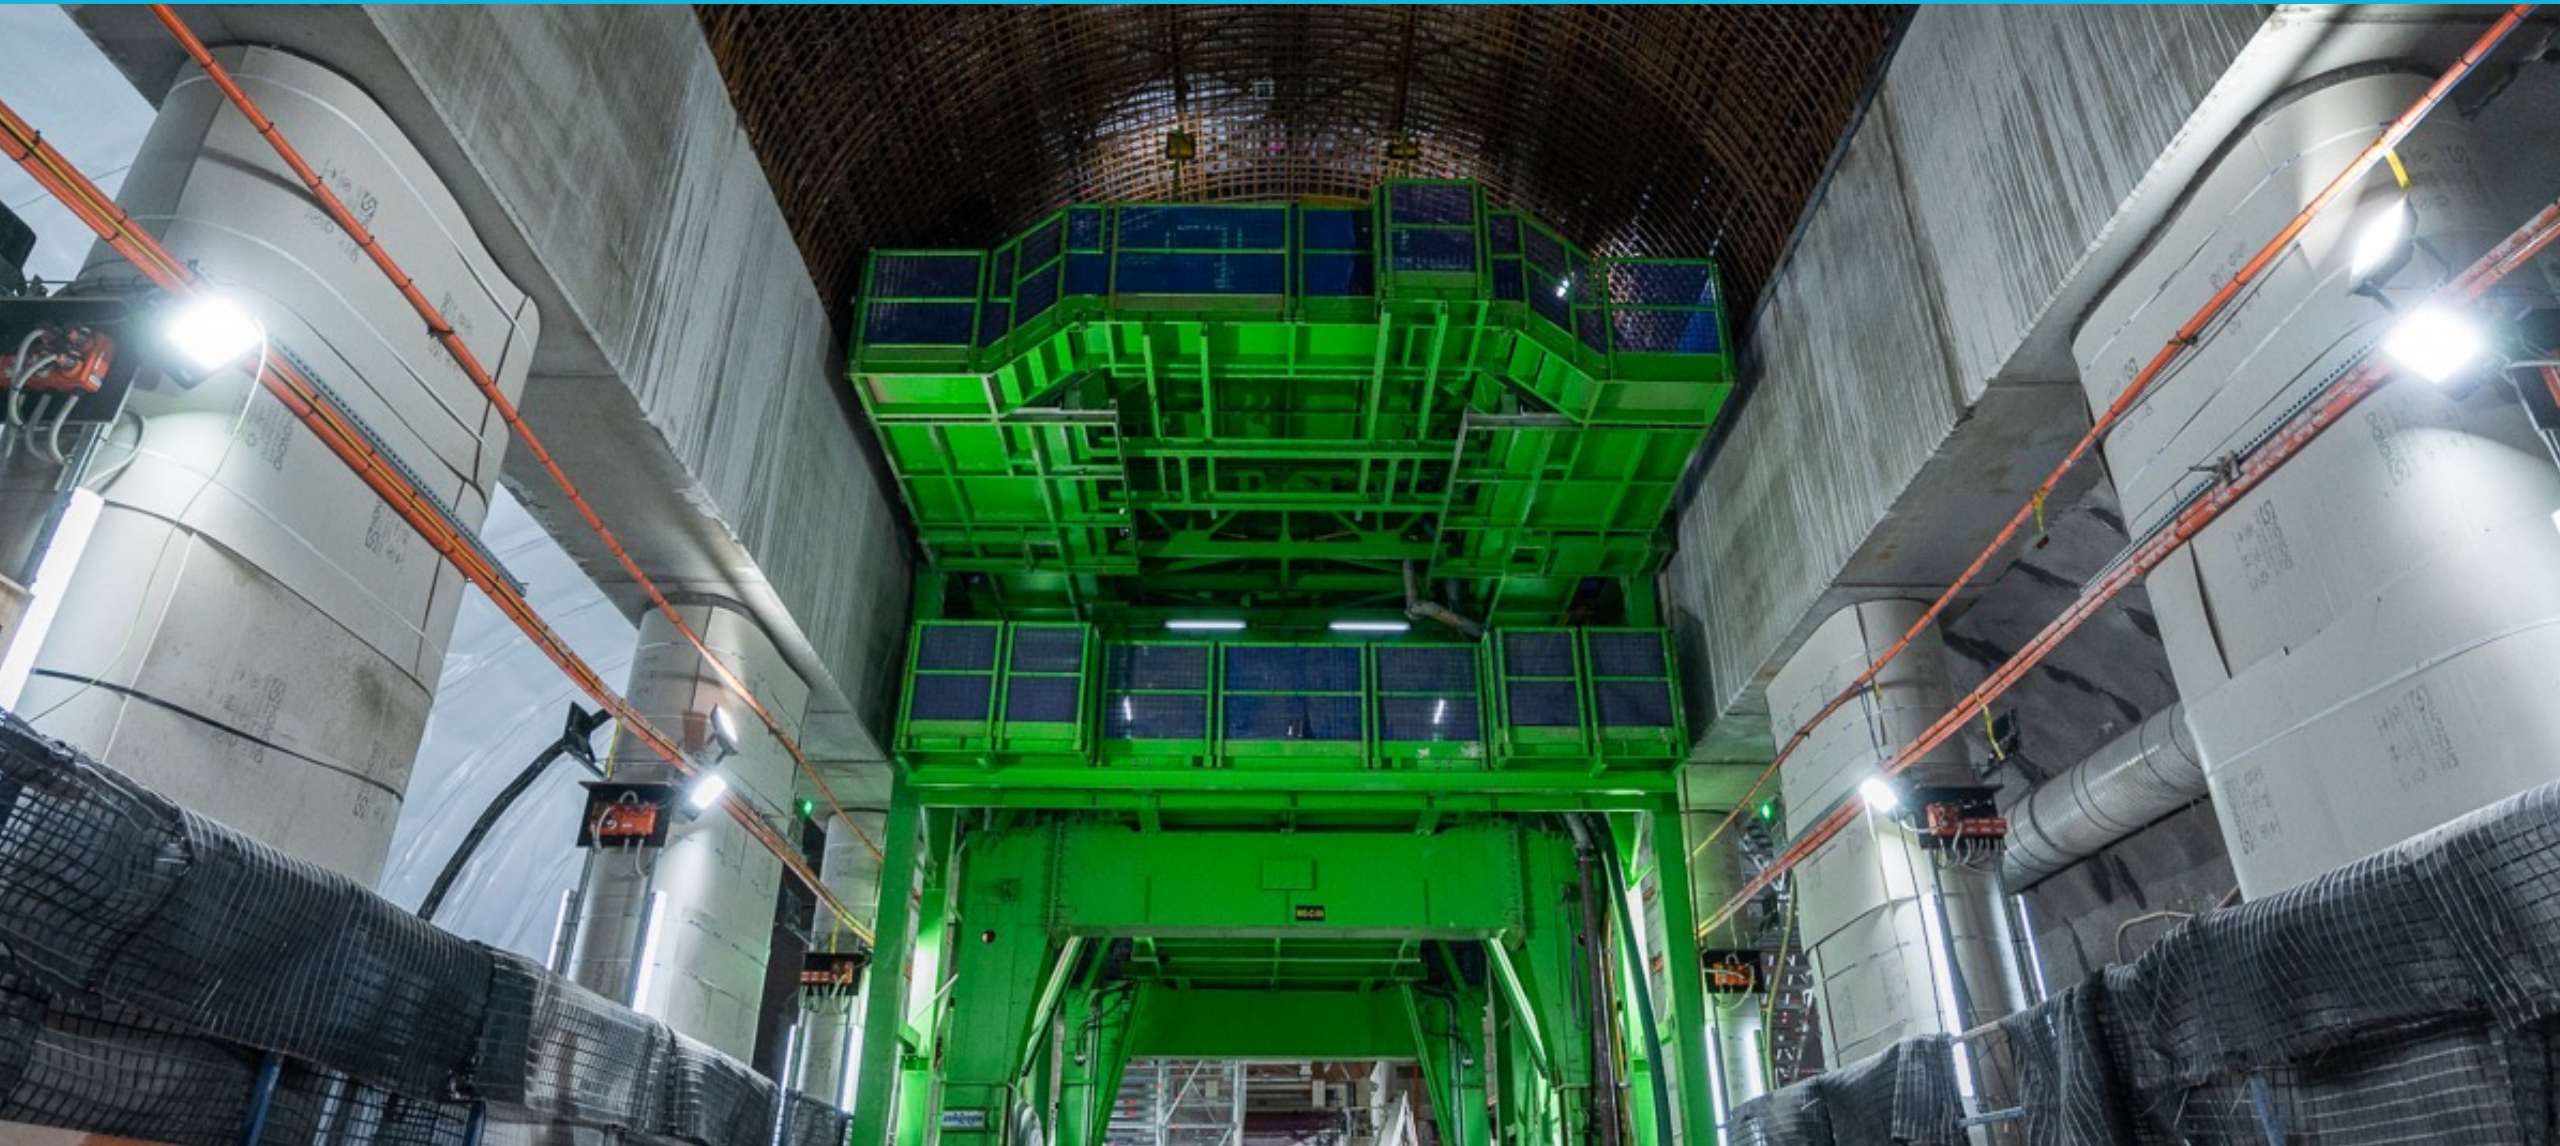


ACTIVITY	2021		2022			
	NOV	DEC	JAN	FEB	MAR	APR
Pile Cap Construction	●.....●					
Tower Crane Install				●.....●		
Collins St Gantry Install					●.....●	
Concrete pumps and loading bays in use					●.....●	
Removal of acoustic shed and deck						●.....● Until July '22
Structures and lining support and bottom-up construction within shed	●.....●		●.....●

Federation Square Site





Federation Square Site



ACTIVITY	2021		2022	
	NOV	DEC	JAN	FEB
Structures and lining support				
Steel Bridge Widening				
Under Track Crossing Excavation				
Under Track Crossing Backfill Removal				
Flinders Street one night closure for plant demobilisation	 28 Nov 9pm – 6am			

Flinders Quarter Site

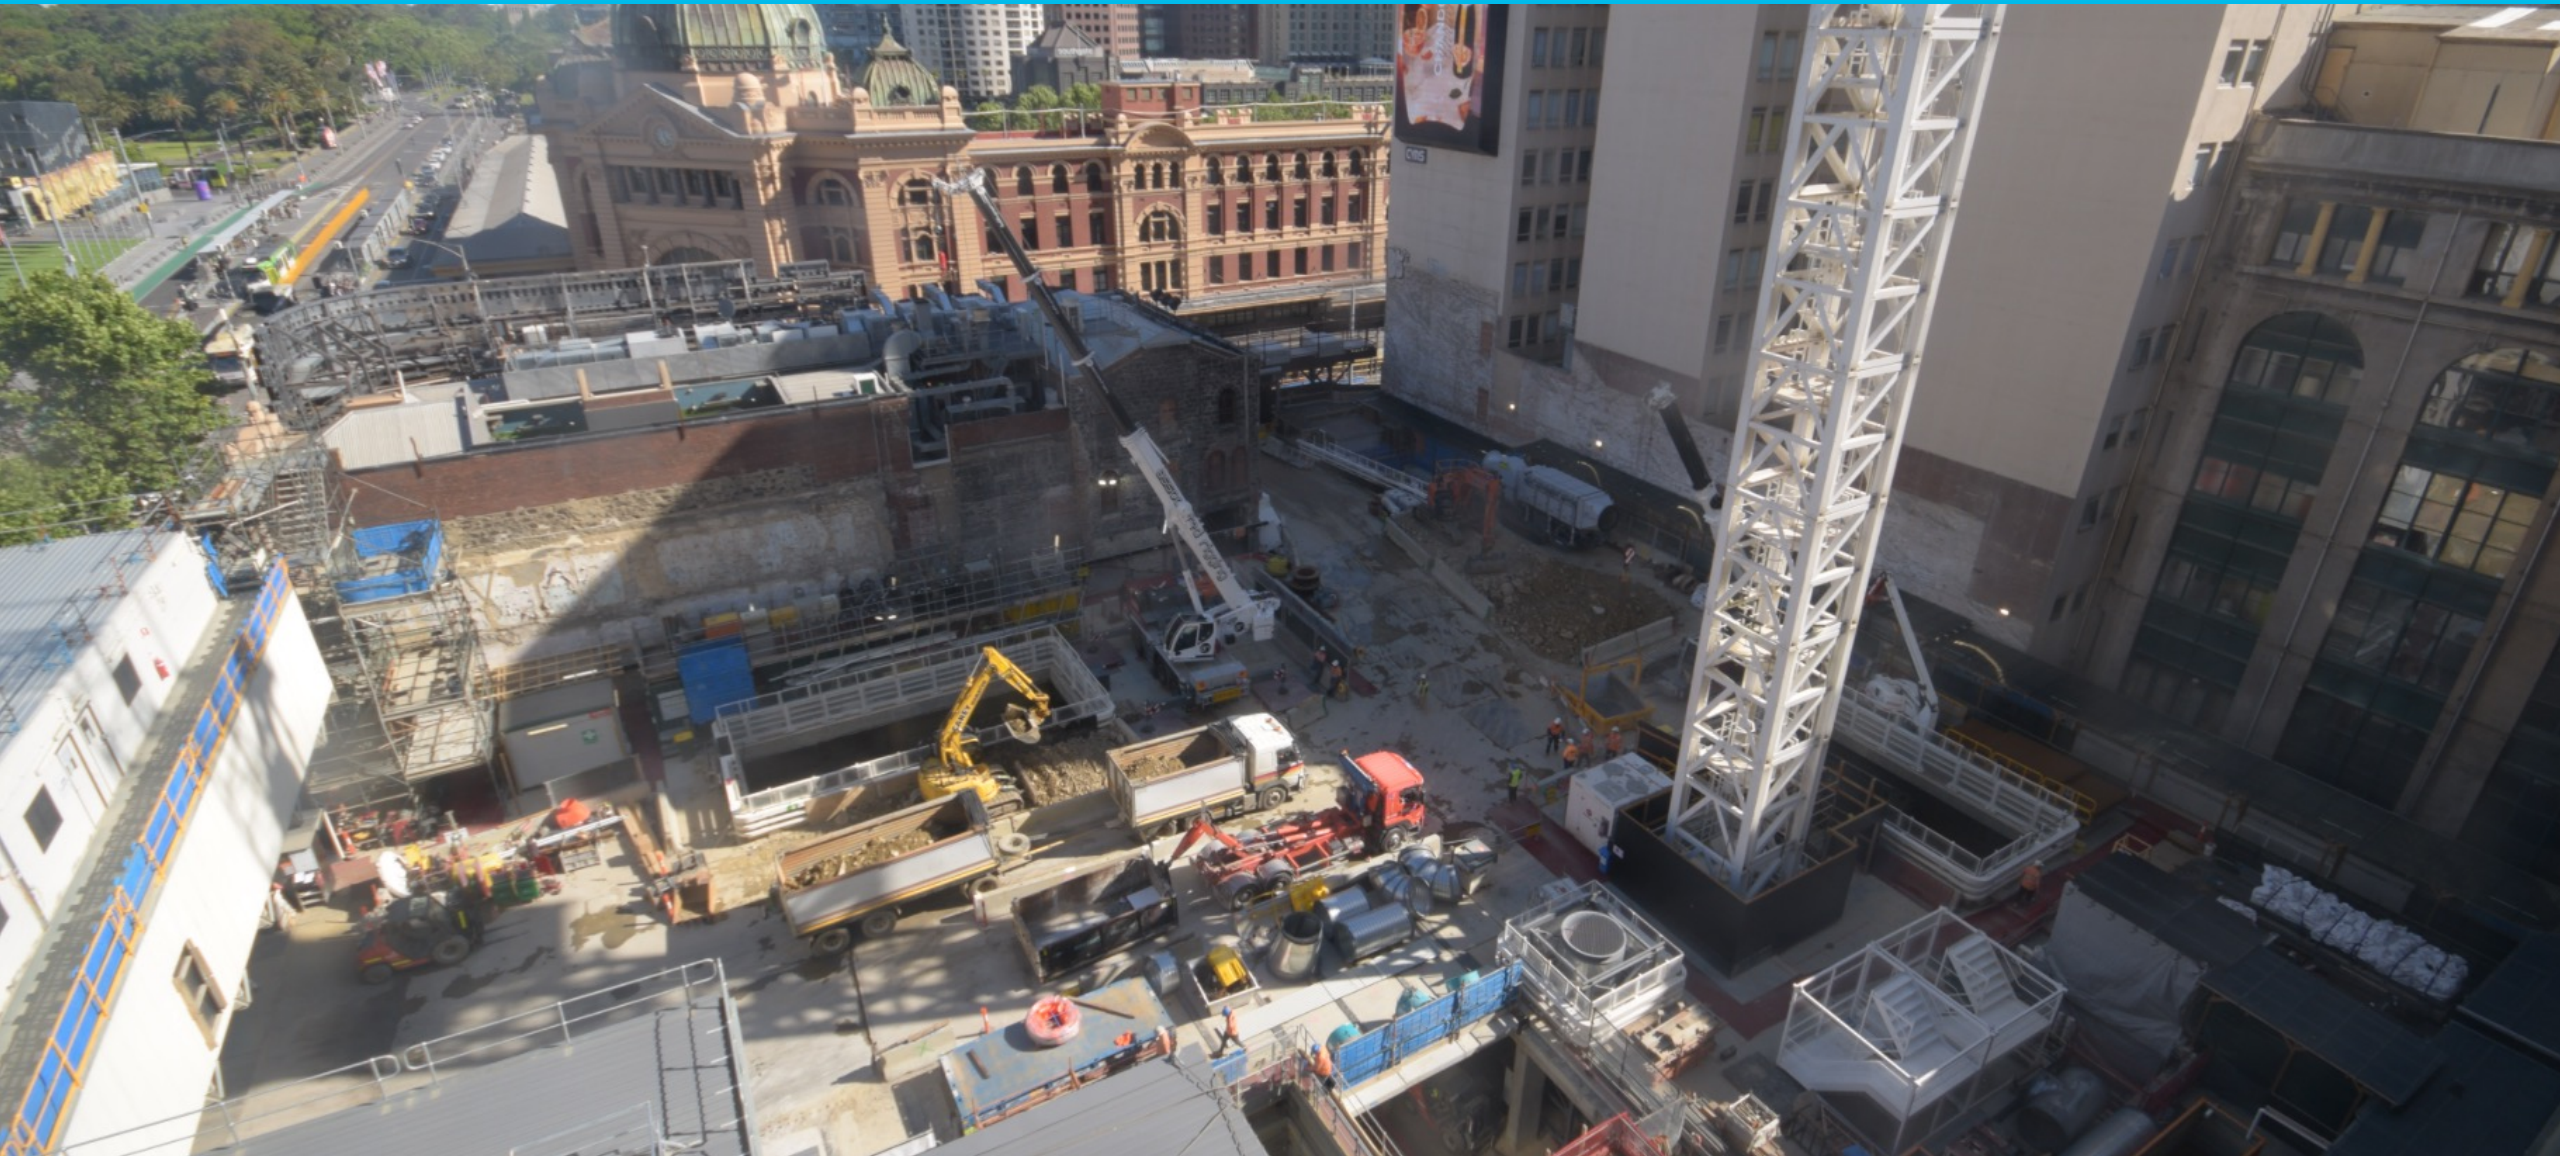

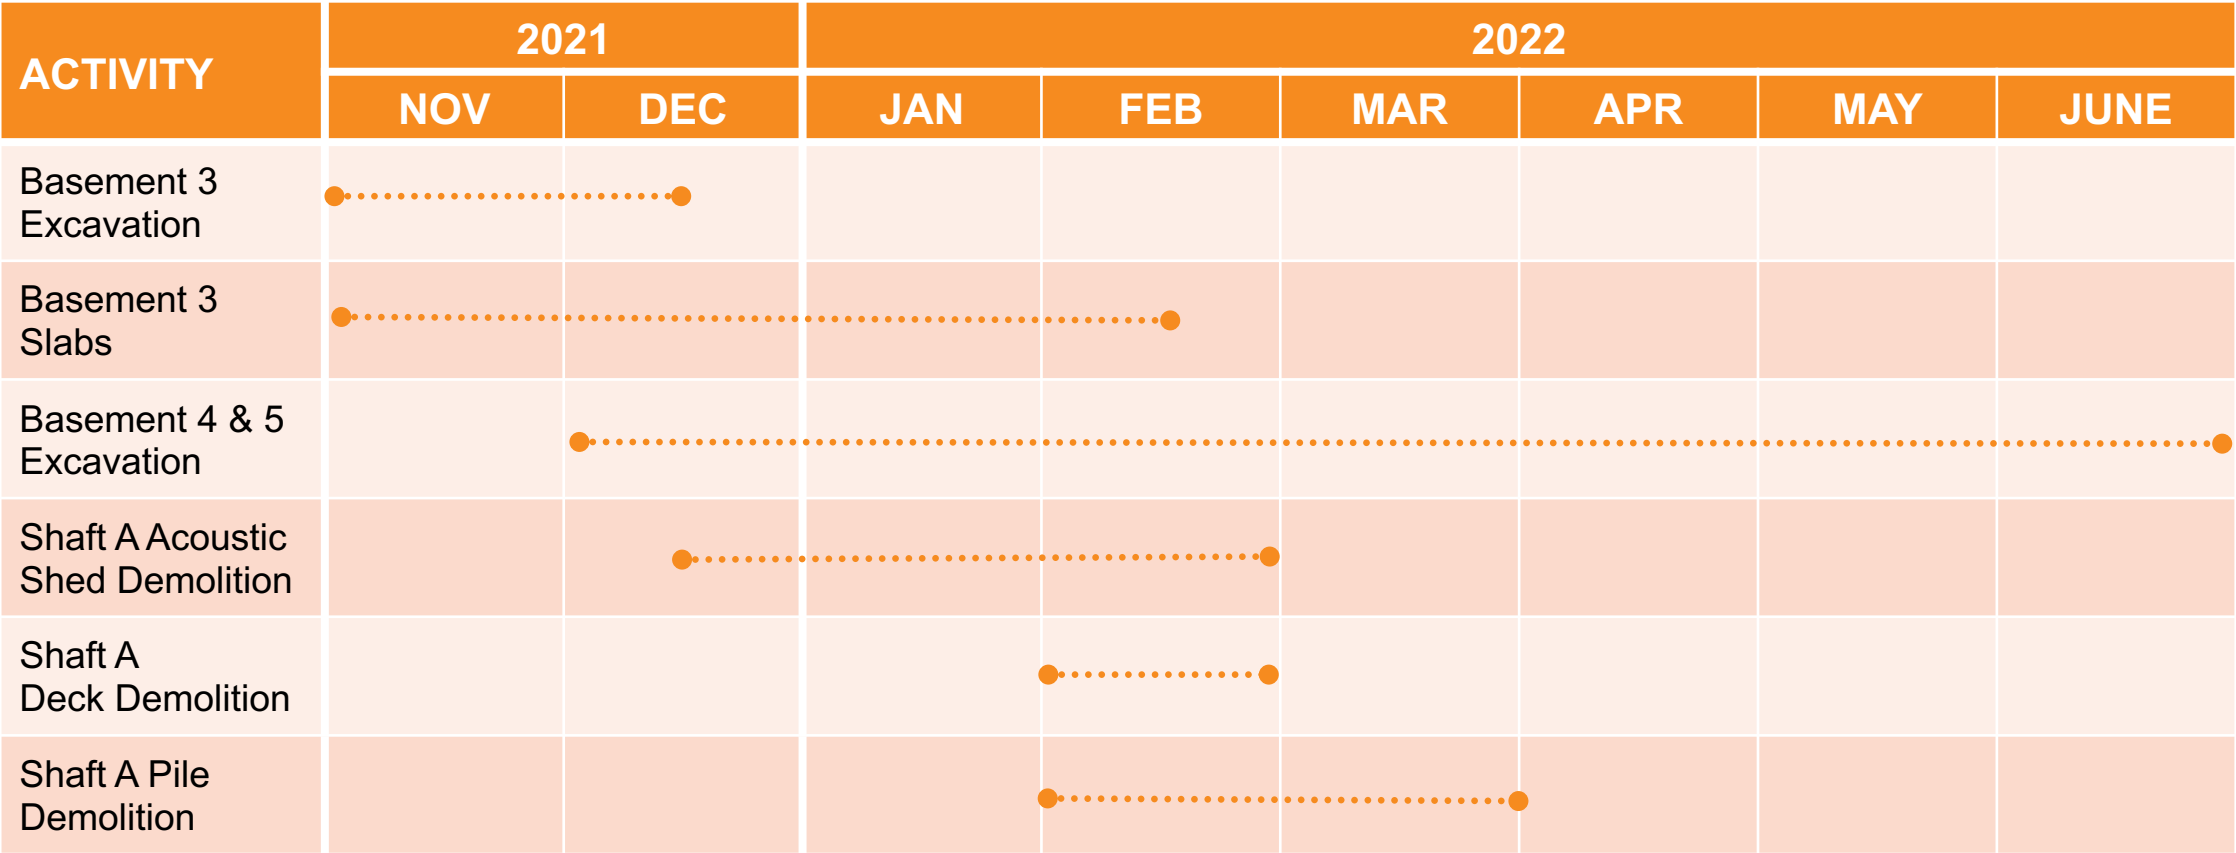

Standard Hours

Monday – Friday

- 7am – 6pm
- Saturdays – 7am – 1pm

Out of Hours

Monday – Friday

- 5am – 7am
- Deliveries and spoil removal

Monday – Friday

- 6pm – 12am
- Excavation hammering until 12am
- Spoil removal until 12am
- Steel fixing, formwork and other low-level noise activities

Saturdays

- 8am – 6pm
- Excavation hammering
- Spoil removal
- Steel fixing and formwork

Sundays

- 8am – 6pm
- Steel fixing and formwork
- Other low-level noise activities

Christmas Shutdown Period



The Metro Tunnel Project will take a break from construction from Wednesday 22 December 2021 to Monday 10 January. With the potential for some works at some sites to recommence from January 5.

The site will be monitored by security during the closure. Members of the project team will be on call during this time. If you have any queries, please phone the Metro Tunnel Project Information Line on **1800 105 105**.



Flinders Link

Flinders Street Staging Update



Flinders Link Pedestrian Connection



- Passengers will be able to switch easily from Metro Tunnel services to the City Loop and other services at Flinders Street Station via the underground Flinders Link (including Campbell Arcade)
- Main construction works to commence, subject to planning approvals, in May 2022
- Heritage permit application to Heritage Victoria
- Advertising and opportunity for public submissions to Heritage Victoria for 10 business days through their website in December 2021.




Legend

-  New station location
-  Flinders Street Station - Direct to platforms

Flinders Link Pedestrian Connection



Design for Campbell Arcade has been enhanced to retain heritage.

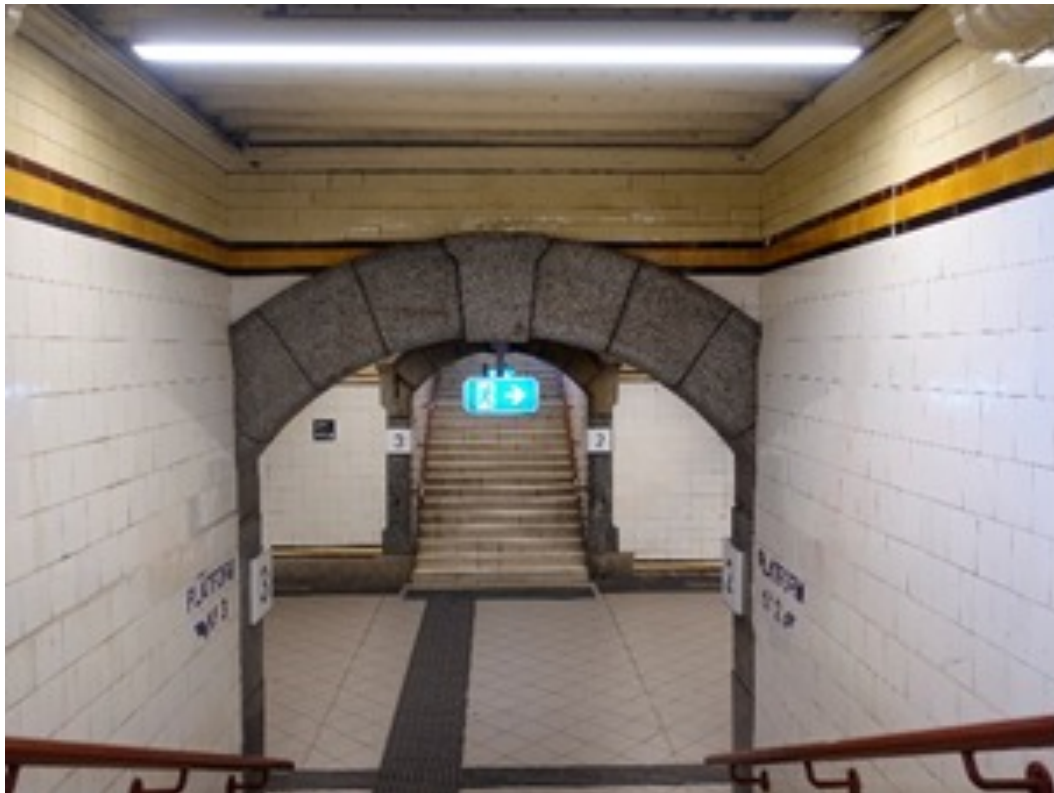

Flinders Link Site



Flinders Link Site

Flinders Street Staging: Present – April 2022




Activities include:

- Complete strut removal and backfill
- Install permanent watermain
- Undertake pile breakback (within the driveway)
- Reinstall pedestrian crossing
- Complete stormwater

Local Impacts:

- Periods of high-level noise during pile breakback
- Hoarding realignment

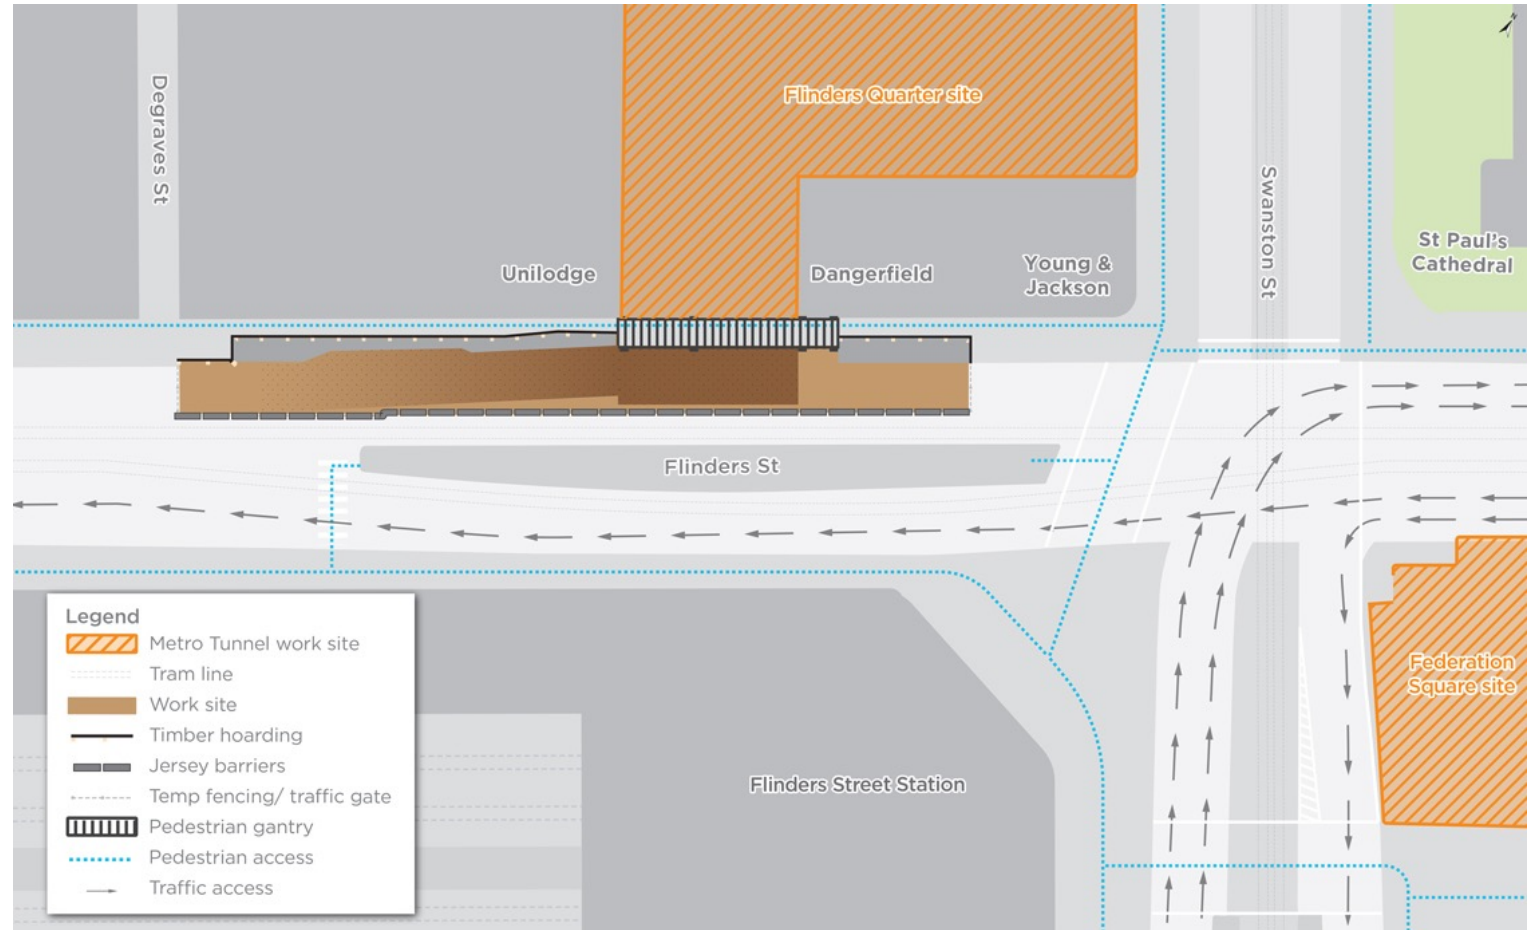

Flinders Link Site

Flinders Street Staging: April to September 2022




Activities Include:

- Stormwater underbore
- Breakback piles, temp slab
- Reinstate utilities (Yarra Trams pit, water main)

Local Impacts

- No traffic or footpath impacts, undertaken pit to pit
- Periods of high-level noise during pile breakback

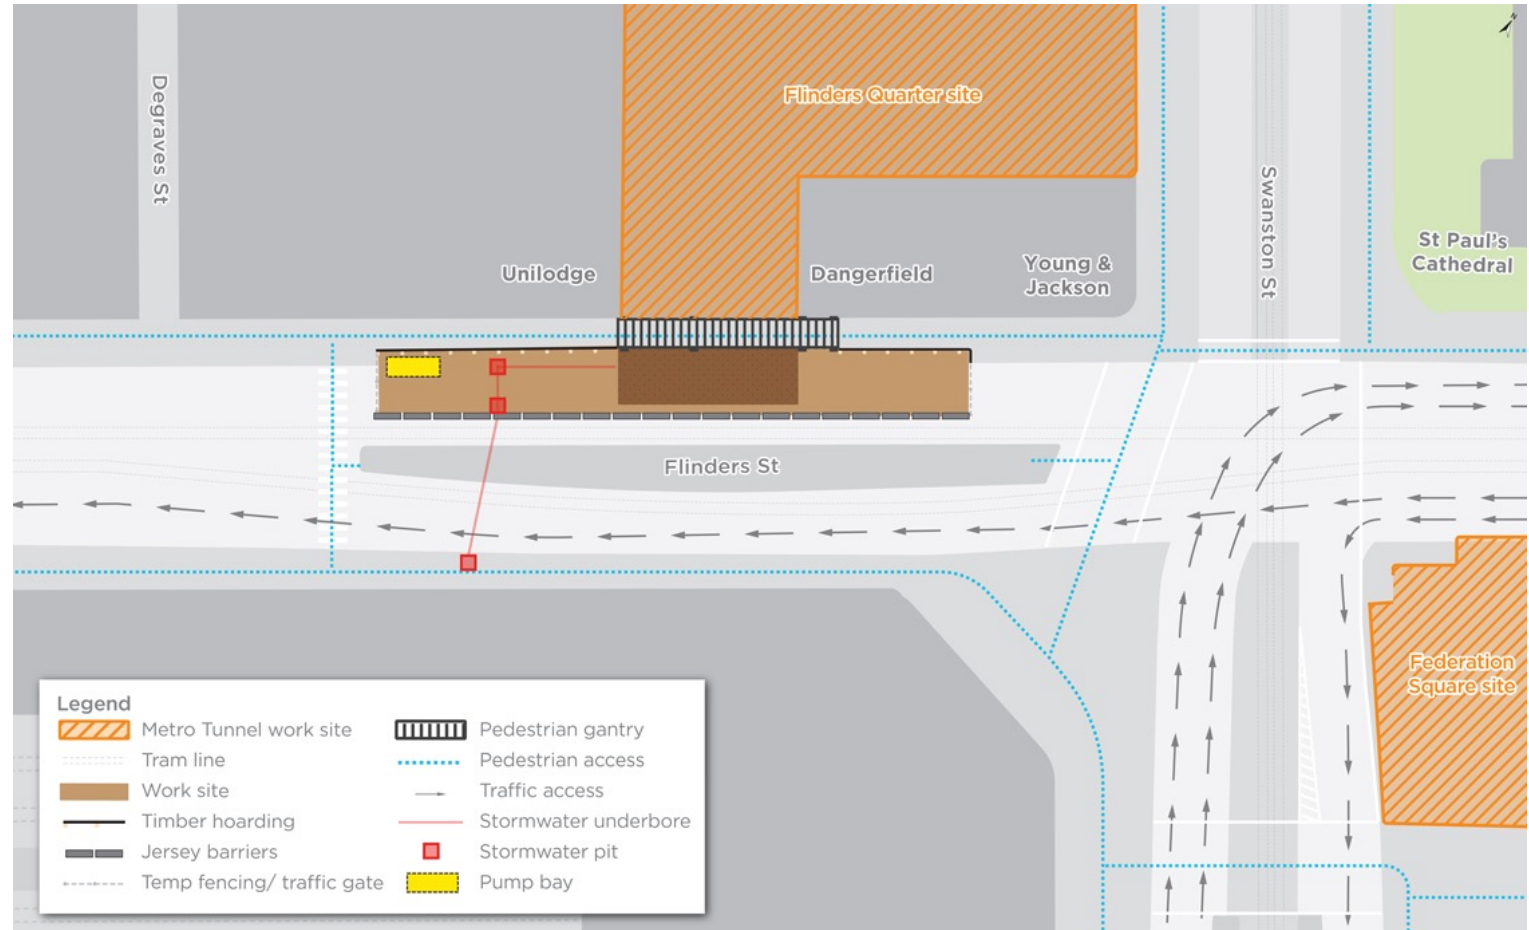

Flinders Link Site

Flinders Street Staging: September to November 2022




Activities Include:

- Close footpath
- Remove gantry
- Breakback piles, temp slab, capping beam in footpath
- Building services entries and connections.
- Install smaller gantry
- Re-open footpath

Local Impacts

- Close Flinders Street footpath for up to 3 months
- Periods of high -level noise during pile breakback

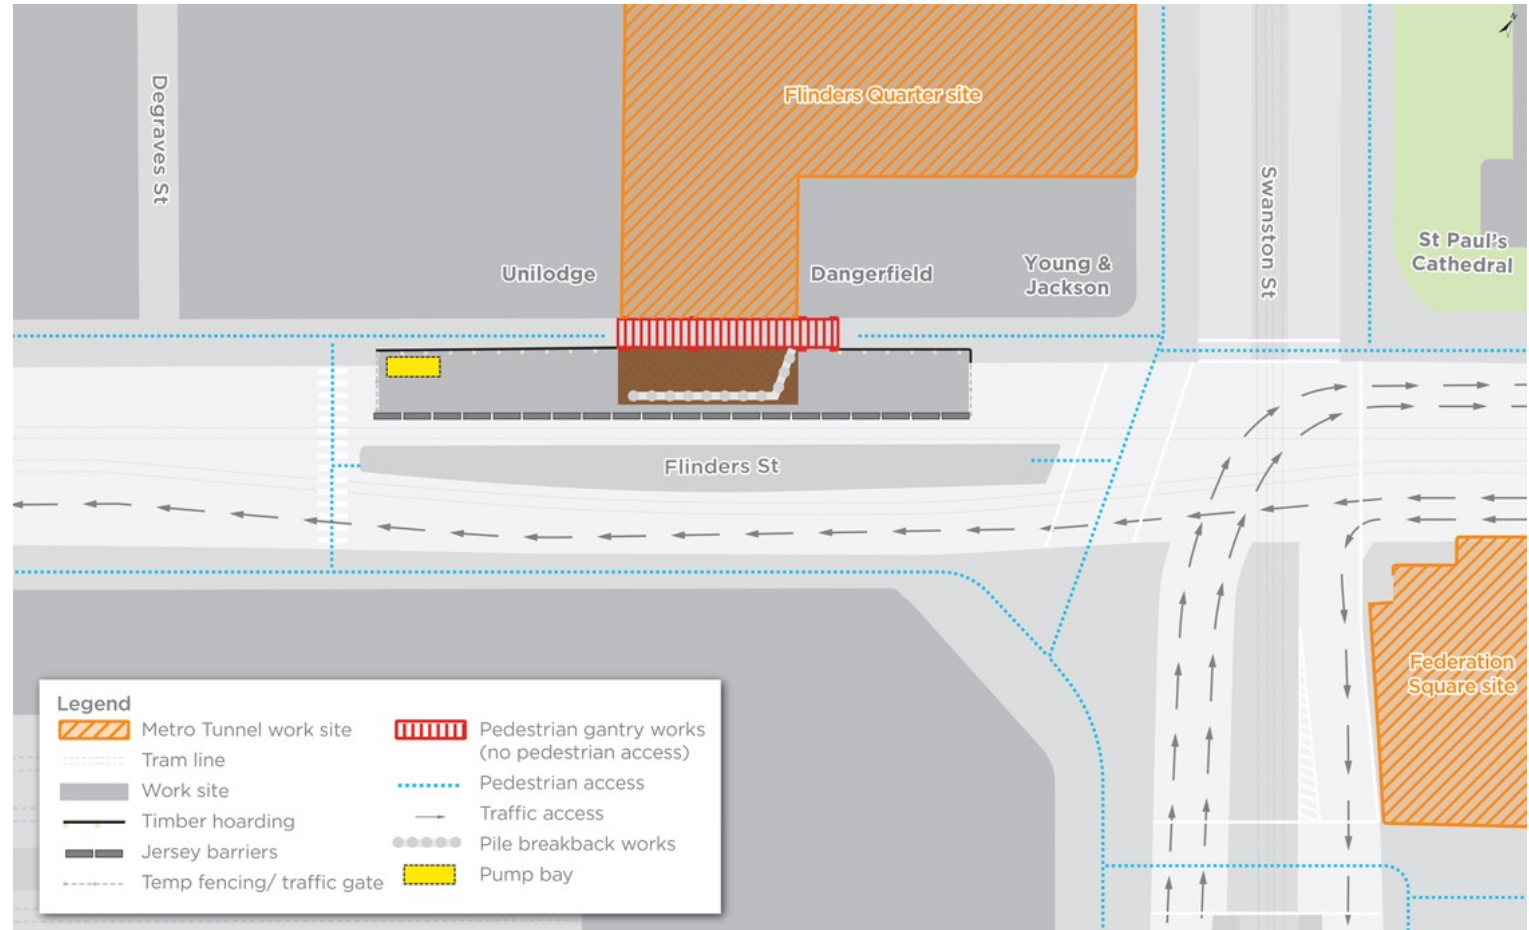

Flinders Link Site

Flinders Street Staging: November 2022 – December 2023




Activities include:

- Reduce hoarding to long term configuration

Local impacts:

- Hoarding remains in place outside 238 Flinders Street
- One lane of Flinders Street eastbound re-opens

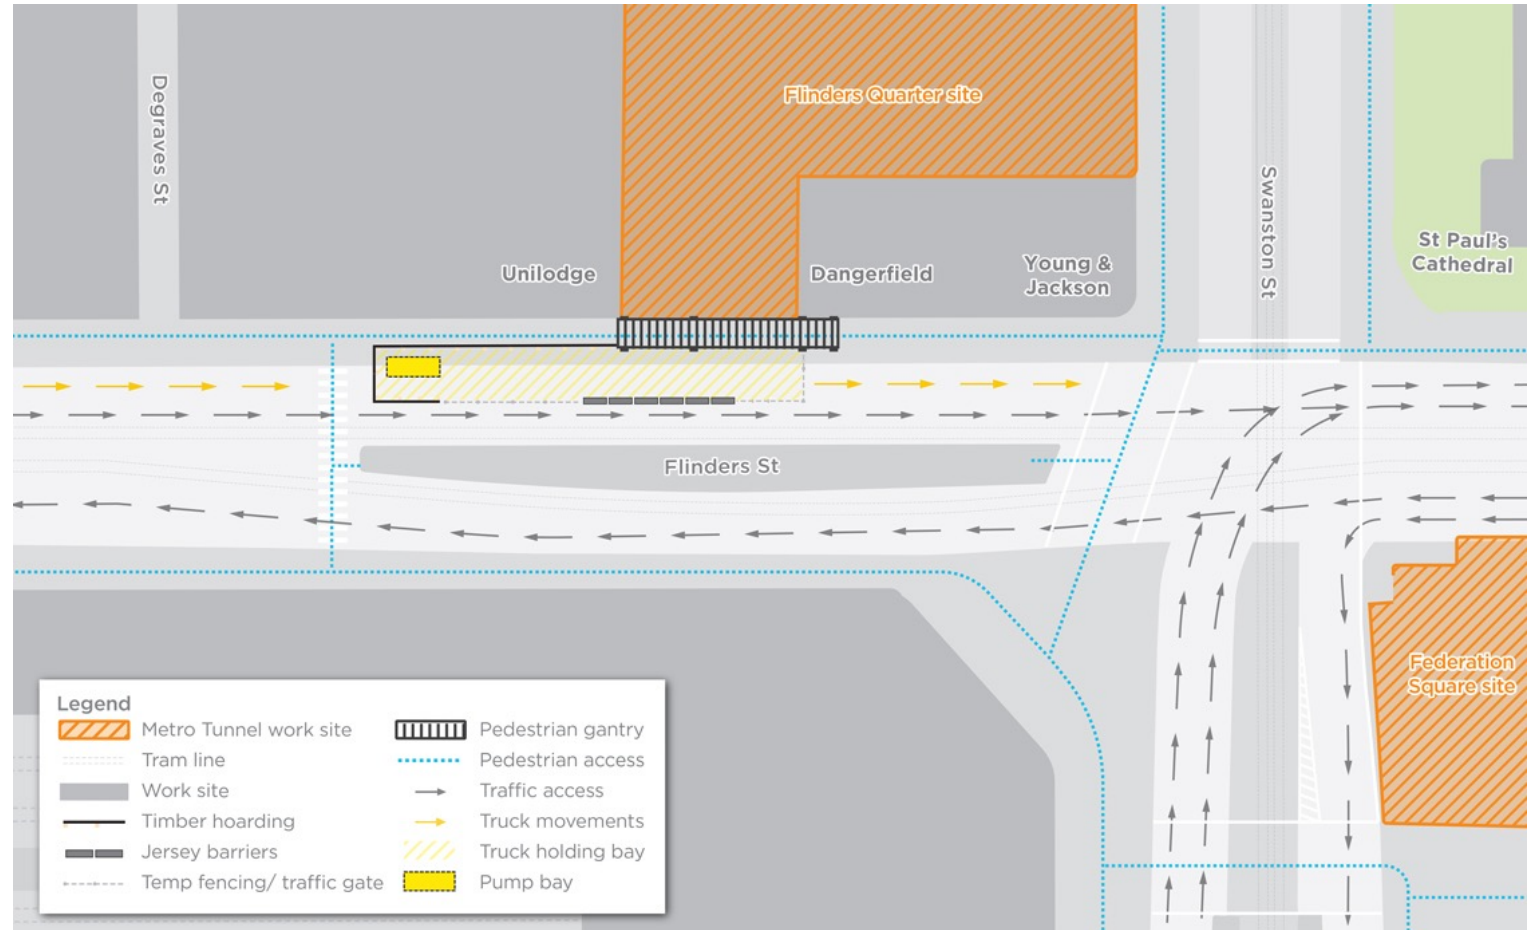

Questions
